INVITATION TO BID

Spring Creek Park Pavilion Structural Repair

PROJECT DETAILS

Project	Spring Creek Park Pavilion Structural Repair
Project Address	4001 S. Himalaya St, Aurora, CO 80013
Date Issued	October 20, 2026
Bid Submission Deadline	November 30, 2026 at 12:00 PM (noon) Mountain Time
Contact Information	Ryan Bailey, Deputy Director, Trails Park and Recreation District
Email	Ryan.Bailey@tprd.org
Telephone	(303) 269-8405

GENERAL INFORMATION

The Trails Park and Recreation District (the "District" or "Owner"), a Colorado Title 32 Special District, is seeking bids from qualified general contractors for the structural repair of the Spring Creek Park Pavilion in Aurora, Colorado. The District serves residents in unincorporated Arapahoe County and Eastern Centennial, providing well-maintained parks, trails, open spaces, and recreational amenities across a 10.5-square-mile area. The District manages 20 developed parks, 25 miles of trails, three facilities (Trails Recreation Center, Lookout Park and Pool, and Trails Skate Park), and over 300 acres of natural areas.

In July 2026, a vehicle left the roadway and struck the Spring Creek Park Pavilion, causing significant structural damage to the northeast corner of the building. Arapahoe County has posted the building as "unsafe to occupy." This Invitation to Bid solicits proposals for the structural repair of the pavilion in accordance with engineered construction documents prepared by Martin/Martin Consulting Engineers. This is an insurance-funded repair. The District's insurer and its adjuster may inspect the work, and the Contractor shall cooperate with reasonable requests for documentation, including progress photographs and itemized invoices. Work outside the awarded scope shall not proceed without a written change order approved by the District.

The purpose of this Invitation to Bid (invitation) is to solicit bids for the Spring Creek Park Pavilion Structural Repair Project. The District intends to award a single contract covering the full scope of repair work

described below. This invitation, including all attachments and addenda, is published on BidNet Direct (www.bidnetdirect.com).

PROJECT DESCRIPTION

The Spring Creek Park Pavilion Structural Repair project involves the repair and reconstruction of the damaged northeast corner of the pavilion and associated interior and site repairs, restoring the building to its pre-damage condition in accordance with 2024 IEBC Chapter 4 (Less Than Substantial Damage).

Scope includes:

- Temporary shoring of existing roof framing during repair work.
- Demolition of damaged concrete masonry unit (CMU) walls at the northeast corner.
- Reconstruction of masonry walls, including new steel reinforcing, lintels, anchor bolts, and post-installed dowels per structural details.
- Repair of existing masonry units to remain, matching existing color, texture, and bond pattern.
- Foundation-level reinforcing dowel work per structural details.
- Replacement of damaged downspouts, gutters, fascia, and soffit as needed to complete the repair.
- Site restoration, including curb, gutter, and sidewalk repair at the two affected locations, asphalt crack repair in the parking lot, and restoration of the damaged landscape planting bed.
- Removal and replacement of damaged paver flooring within the pavilion, patched to match existing.
- Cleaning, staining, and finishing of the pavilion's wood ceiling and trim, including replacement of damaged boards to match existing.
- Removal, protection, and reinstallation of interior and exterior surveillance cameras as required for the work, with each reinstalled camera tested to confirm proper function.
- Replacement of the damaged restroom steel door, hinges, and lockset, and repair of hairline masonry cracking in the restroom.
- Repair of the front entrance ceiling, including replacement of the recessed light fixture, trim, and drywall, textured and painted to match existing.
- Replacement and installation of the damaged pavilion trash receptacle to match existing.
- Evaluation of the 10' x 10' roll-up door and keyless entry pad, with repair as required to restore proper operation. Full replacement shall be priced as a separate alternate.
- Debris removal and final construction cleaning of the pavilion and affected areas.

SCOPE OF WORK

The scope of work is defined by the structural construction documents prepared by Martin/Martin Consulting Engineers (Project No. 26.1101.S.01, dated 9/16/2026), attached to this invitation.

The scope of work includes, but is not limited to, the following:

1. **Permitting and Site Preparation:**

- Work with the Owner, structural engineer, and Arapahoe County to ensure all permits and regulatory requirements are satisfied.
- Engage a Colorado-licensed Professional Engineer to design temporary shoring required to support existing roof framing during repair. Shoring shall remain in place until repairs are complete, fully cured, and have passed inspections.
- Remove the existing emergency shoring and temporary framing installed following the incident, coordinated with installation of the engineered temporary shoring.
- Appropriate site preparation and protection of surrounding park areas.

2. **Demolition and Removal:**
   - Removal of damaged masonry, framing, and related building elements as specified.
   - Proper disposal of all debris.
3. **Construction:**
   - Execution of structural repair and reconstruction as defined by the engineered structural drawings.
   - Coordination of masonry block, mortar color, and texture samples with the District for approval prior to procurement.
   - Coordination with the District's separately retained special inspection agency, as required for Level 2 special inspections under the structural drawings. The Contractor shall request and schedule all required inspections, and the cost of any additional testing or inspection resulting from corrective work shall be borne by the Contractor.
   - Preparation of all submittals required by the structural drawings, including product data (masonry block, reinforcing, and anchor bolts), mortar and grout mix designs, and reinforcing steel shop drawings per ACI 315. All submittals shall be in electronic format.
   - Construction of a masonry sample panel, minimum 4 feet by 4 feet, for acceptance prior to proceeding with masonry work.
   - Photo documentation of the existing below-grade masonry to remain, submitted to the structural engineer for evaluation prior to installing adhesive dowels.
   - Re-establishment of existing masonry control joints, including exterior sealant to match existing conditions, with the product submitted to the District for approval.
   - Field verification of existing structural conditions. The Contractor shall notify the structural engineer of any conditions that differ from the drawings and allow for their resolution in the construction schedule.
   - Protection and retention of existing top plates, wood framing, and connections. The Contractor shall notify the structural engineer of any damage.
4. **Post-Construction:**
   - Final site clean-up and disposal of construction waste.
   - Delivery of "as-built" plans and warranties.

- Participation in the final inspection and punch list process, and coordination of Arapahoe County's final sign-off to lift the "unsafe to occupy" posting.

SCHEMATIC DRAWINGS AND ENGINEERING PLANS

Detailed structural construction documents are attached to this invitation (Sheets S0.1, S0.2, S1.0, S2.0, Martin/Martin Project No. 26.1101.S.01).

The insurance adjuster's scope of repairs (Engle Martin, Estimate No. 1000574928) is attached for reference only. Quantities shown are estimates; bidders are responsible for verifying all quantities and conditions. Where the scope of repairs differs from the structural drawings or this invitation, the structural drawings and this invitation govern.

SITE TOUR

A site tour will be held for interested bidders at 1:00 PM Mountain Time on Wednesday, November 4, 2026, at the project site, Spring Creek Park Pavilion, 4001 S. Himalaya St, Aurora, CO 80013. Attendance is mandatory. The pavilion is posted unsafe to occupy; bidders may enter the damaged area only during the scheduled site tour and when accompanied by District staff.

QUESTIONS

The cutoff time for questions regarding the project and bid packet is 5:00 PM Mountain Time on Tuesday, November 10, 2026. Answers to all questions received will be issued by addendum no later than Thursday, November 12, 2026. All questions must be submitted in writing through the BidNet Direct question-and-answer feature for this solicitation. Replies will be issued only by written Addenda. Only questions answered by formal written Addenda will be binding. Oral and other interpretations or clarifications will be without legal effect.

Addenda will be posted on BidNet Direct, which will notify all registered plan holders. Bidders are responsible for checking BidNet Direct for addenda and shall acknowledge all addenda in their bid. No Addenda will be issued later than three (3) days prior to the date for receipt of Bids except an Addendum, if necessary, postponing the date for receipt of Bids or withdrawing the request for Bids.

For any questions regarding the engineered structural plans, please contact Greg Rademacher at Martin/Martin Consulting Engineers, (303) 431-6100 ext. 587.

BID AND CONTRACT DOCUMENTS

The Bidding and Contract Documents, including the structural drawing set and all addenda, are available for download on BidNet Direct. Submittal requirements are outlined in the Bid Submittal Requirements below.

INSURANCE AND BONDS

The successful bidder shall maintain, at a minimum, Commercial General Liability insurance of $1,000,000 per occurrence and $2,000,000 aggregate, Automobile Liability insurance of $1,000,000 combined single limit, and Workers' Compensation insurance at statutory limits. The Trails Park and Recreation District shall be named as an additional insured on the General Liability and Automobile Liability policies, and a certificate of insurance shall be provided prior to contract execution.

A performance, payment and warranty bond in the full amount of the contract price shall be required of the successful bidder prior to commencing work, in accordance with C.R.S. § 38-26-106.

QUALIFICATIONS

The contractor shall be a general contractor holding a current contractor license (or able to obtain one prior to permit application) that has been in business and in continuous operation for a minimum of 4 years. The contractor shall be able to provide evidence of a minimum of 3 similar completed projects within the past 5 years. To qualify, projects shall meet the following criteria:

- Structural repair or reconstruction of reinforced concrete masonry unit (CMU) construction.
- Experience coordinating with a licensed structural engineer of record and a third-party special inspection agency.
- Experience obtaining permits and inspections through a local building department following structural damage or a red-tag condition.

> **Note:** Experience with insurance-funded structural repair projects should be highlighted.

BID SUBMITTAL REQUIREMENTS

All of the following, together with the documents required under Bid Submission Instructions and acknowledgment of all addenda, are required for bids to be considered complete:

1. Completed, itemized bid pricing covering the full scope of work, broken out separately as follows:
    - Shoring (design, installation, and removal, including removal of existing emergency shoring)
    - Demolition
    - Masonry reconstruction (materials and labor, including reinforcing, lintels, and anchor bolts)
    - Repair of existing masonry to remain
    - Foundation/dowel work
    - Site restoration (curb, gutter, and sidewalk)
    - Downspout, gutter, fascia, and soffit repair

- Pavilion pavers, wood ceiling, front entrance ceiling and light fixture, trash receptacle, and surveillance camera removal/reinstallation
- Restroom door replacement and roll-up door repair
- Alternate: Roll-up door and keyless entry pad full replacement
- Asphalt crack repair and landscape restoration
- Permits and fees
- General conditions, mobilization, overhead and profit

2. Proposed project schedule, including major milestones (permit submittal, shoring installation, demolition, masonry reconstruction with cure time, inspections, final completion).
3. Three project descriptions with references illustrating contractor's qualifications (see minimum qualifications above). Project information shall include at a minimum:
    - Name of Project
    - Project/Client reference (name, title, email, telephone number, and description of project role)
    - Brief description (1 paragraph) of project, including nature of project, contractor's role, and total construction cost. Project photographs may be attached if desired.

BIDDER'S RESPONSIBILITIES

Before submitting a Bid, each Bidder must (a) examine the Contract Documents thoroughly; (b) familiarize itself with local conditions that may in any manner affect cost, progress, or performance of the Work (attendance at the scheduled site tour is mandatory); (c) familiarize itself with Federal, State, and local laws, ordinances, rules, and regulations that may in any manner affect cost, progress, or performance of the Work; (d) study and carefully correlate Bidder's observations with the Contract Documents. The submission of a Bid will constitute an incontrovertible representation by the Bidder that the Contract Documents are sufficient in scope and detail to indicate and convey understanding of all terms and conditions for performance of the Work.

Contractor shall engage, at its own cost, a Colorado-licensed Professional Engineer to design the temporary shoring required to support existing roof framing during the repair, as described in the Scope of Work. Any Contractor-requested change from the structural drawings must be approved and designed by Martin/Martin Consulting Engineers prior to proceeding, and Contractor shall compensate Martin/Martin Consulting Engineers for any such design changes. Changes initiated by the District or required by concealed or differing site conditions shall be addressed by change order.

AWARD

The Owner will review bids, and award results will be posted on BidNet Direct. The District will select the bid that offers the overall best value, based on the Evaluation Criteria set forth below. No bids may be withdrawn for a period of sixty (60) days following the bid submission deadline.

Please note the Trails Park and Recreation District is a tax-exempt organization. A certificate of exemption is available by request.

The successful bidder will be required to execute the District's standard project agreement. Substantial completion of the building repairs shall be achieved within ninety (90) calendar days after issuance of the building permit. Site work that cannot be performed due to seasonal temperature limitations, including concrete curb, gutter, and sidewalk replacement, asphalt crack repair, and landscape restoration, shall be completed no later than May 31, 2027. The completion time will be extended for delays caused by abnormal weather conditions, provided the Contractor requests the extension in writing within seven (7) days of the delay and documents the conditions; weather typical of the season shall not be grounds for an extension. The Contractor shall warrant all workmanship and materials for a minimum of one (1) year from the date of final acceptance.

> All bids must be submitted through BidNet Direct no later than 12:00 PM (noon) Mountain Time on Monday, November 30, 2026. Submissions received after this date and time will not be considered.

BID SUBMISSION INSTRUCTIONS

All bids shall be submitted electronically through BidNet Direct in the form of one PDF document no later than 12:00 PM (noon) Mountain Time on Monday, November 30, 2026. Emailed, mailed, or hand-delivered bids will not be accepted. Each bid shall include documentation of the bidder's eligibility to perform work and obtain building permits (such as a current contractor license), a current certificate of insurance, and a letter from a surety confirming the bidder's ability to furnish the required performance, payment and warranty bond.

EVALUATION CRITERIA

Bids will be evaluated based on the following criteria:

- Compliance with bid requirements.
- Relevant experience and qualifications.
- Proposed approach and timeline.
- Cost effectiveness.
- References and past performance.

> **Attachments:** Structural Drawing Set (Sheets S0.1, S0.2, S1.0, S2.0 — Martin/Martin Project No. 26.1101.S.01); Engle Martin Scope of Repairs (reference only)

SPRING CREEK PARK / PAVILION
VEHICLE STRIKE REPAIR


4001 SOUTH HIMALAYA STREET
AURORA, COLORADO 80013

MARTIN/MARTIN PROJECT NO. 26.1101.S.01
FOR CONSTRUCTION SET: 09/16/2026

AERIAL PHOTO



VICINITY MAP

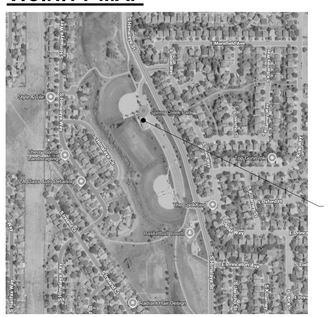

CONSULTANT

MARTIN/MARTIN
CONSULTING ENGINEERS

12499 WEST COLFAX AVENUE, LAKEWOOD, COLORADO 80215
MAIN 303.431.6100 MARTINMARTIN.COM

CONTACT: GREG RADEMACHER
GRADEMACHER@MARTINMARTIN.COM
303.431.6100 EXT. 587

OWNER'S REPRESENTATIVE

TRAILS PARK AND RECREATION DISTRICT

16799 EAST LAKE AVENUE
CENTENNIAL, COLORADO 80016

CONTACT: RYAN BAILEY
RYAN.BAILEY@TPRD.ORG
303.269.8405

DRAWING INDEX

SHEET NUMBER	SHEET TITLE
S0.1	GENERAL NOTES
S0.2	SPECIAL INSPECTIONS
S1.0	PARTIAL PLANS
S2.0	DETAILS



© MARTIN/MARTIN 2023

SYMBOL LEGEND

SYMBOL	DESCRIPTION
-	GRID LINES
X / XX	SECTION OR DETAIL CUT / SHEET NUMBER
X / XX	ELEVATION CUT / SHEET NUMBER
XXX'-XX"	ELEVATION CALLOUT
X	DRAWING REVISION NUMBER
	CURRENT REVISION CLOUD
	WELDED WIRE REINFORCEMENT
	STEP
	SLOPE
1	KEY NOTE

SYMBOL	DESCRIPTION
X	EXISTING GRID LINES
	EXISTING ELEMENTS (HALFTONE)
	NEW ELEMENTS
X'-XX"	DIMENSIONS TO EXISTING STRUCTURE, FIELD VERIFY (ITALICS)
X'-XX"	DIMENSIONS TO NEW STRUCTURE
	EXISTING LINES (HALFTONE)
(E) TEXT	EXISTING CONDITON NOTES (ITALICS)

NOTES:

1. ITEMS NOT DESIGNED BY M/M ARE SHOWN HALFTONED
   A. ITEMS INCLUDE:
      a. EXISTING CONSTRUCTION

MASONRY NOTES

1) DESIGN STRENGTH:

1A) MASONRY BLOCK, MORTAR, GROUT
- CONCRETE MASONRY UNIT (CMU) STRENGTH = 2,000 PSI (ASTM C90), LIGHTWEIGHT
- MORTAR REQUIREMENT = TYPE S MORTAR (ASTM C270)
- GROUT REQUIREMENT = 2,000 PSI 28-DAY STRENGTH (ASTM C476)

- CONTRACTOR COORDINATE REPLACEMENT BLOCK AND MORTAR COLOR, TEXTURE, AND AESTHETICS WITH OWNER. SUBMIT SAMPLES TO OWNER FOR APPROVAL PRIOR TO PROCUREMENT.

1B) STEEL REINFORCING:
- PRIMARY REINFORCING: ASTM A615, 60 KSI
- HORIZONTAL JOINT REINFORCING: ASTM A951, PREFABRICATED, LADDER TYPE

2) INSTALLATION REQUIREMENTS:

2A) GROUT SOLID ALL CELLS.

2B) INSTALL BLOCK IN RUNNING BOND, TO MATCH EXISTING CONDITIONS.

2C) PROVIDE GROUT WITH SLUMP OF 8 TO 11 INCHES FOR GROUT LIFT HEIGHTS LESS THAN 5'-4" OR 10 TO 11 INCHES FOR GROUT LIFT HEIGHTS GREATER THAN 5'-4" AS MEASURED ACCORDING TO ASTM C143. PROVIDE CLEANOUTS IN THE BOTTOM COURSE OF MASONRY FOR EACH GROUT POUR WHEN THE GROUT LIFT HEIGHT EXCEEDS 5'-4".

3) FACE SHELL REPAIRS:

- EXTEND DEMOLITION OF DAMAGED FACE SHELLS TO EXISTING MORTAR LINES, SET REPLACEMENT MASONRY FACE SHELLS IN NEW MORTAR AND RE-ESTABLISH EXISTING MORTAR LINES.
- DO NOT DAMAGE EXISTING STEEL REINFORCING OR EXISTING GROUT.

SHORING NOTES

1) GENERAL:

1A) CONTRACTOR SHALL PROVIDE AND INSTALL SHORING AS NOTED IN DRAWINGS AND AS DIRECTED BY ENGINEER.

1B) ALL SHORING SHALL BE DESIGNED BY A PROFESSIONAL ENGINEER REGISTERED AND LICENSED IN THE STATE OF COLORADO. ASSUME 1,500PSF ALLOWABLE BEARING PRESSURE BELOW SHORING POSTS FOR DESIGN

1C) ALL SHORING SHALL REMAIN IN PLACE UNTIL REPAIRS ARE COMPLETE, FULLY CURED, AND HAVE PASSED INSPECTIONS.

DESIGN CRITERIA

1) CODES AND STANDARDS:

1A) GENERAL DESIGN
- INTERNATIONAL EXISTING BUILDING CODE (IEBC) 2024
- PROJECT CONSISTS OF REPAIRS FOR LESS THAN SUBSTANTIAL DAMAGE AND DAMAGED ELEMENTS ARE BEING RESTORED TO THEIR PREDAMAGED CONDITION IN ACCORDANCE WITH 2024 IEBC CHAPTER 4.

GENERAL NOTES

1) GENERAL:

1A) ENGINEER: REFERENCES ON THE STRUCTURAL DRAWINGS TO 'ENGINEER' MEAN THE STRUCTURAL ENGINEER OF RECORD. OTHER ENTITIES ARE SPECIFICALLY NOTED AS "CONTRACTOR'S ENGINEER", "MECHANICAL ENGINEER", ETC.

2) USE OF DRAWINGS:

2A) DO NOT SCALE DRAWINGS.

2B) DETAILS ON DRAWINGS TAKE PRECEDENCE OVER GENERAL NOTES AND TYPICAL DETAILS.

2C) DETAILS NOTED TYPICAL APPLY TO ALL SIMILAR CONDITIONS. WHERE NO SPECIFIC DETAILS ARE SHOWN, CONSTRUCTION SHALL CONFORM TO SIMILAR WORK ELSEWHERE ON THE PROJECT.

2D) WHERE DISCREPANCIES OCCUR BETWEEN PLANS, DETAILS AND GENERAL NOTES:
-CONTACT THE ENGINEER PRIOR TO PROCEEDING WITH CONSTRUCTION
-THE MORE STRINGENT REQUIREMENTS SHALL GOVERN FOR BIDDING / PRICING

3) EXISTING STRUCTURES:

3A) CONTRACT DOCUMENTS HAVE BEEN PREPARED USING AVAILABLE DRAWINGS AND SITE OBSERVATION AS PERMITTED BY ACCESS RESTRICTIONS DURING DESIGN.

3B) DURING CONSTRUCTION, THE CONTRACTOR MAY ENCOUNTER EXISTING CONDITIONS WHICH ARE NOT KNOWN OR ARE AT VARIANCE WITH PROJECT DOCUMENTATION. CONTRACTOR SHALL NOTIFY THE ENGINEER OF ALL CONDITIONS NOT PER THE CONTRACT DOCUMENTS. EXAMPLES INCLUDE:
-SIZES OR DIMENSIONS OTHER THAN THOSE SHOWN
-DAMAGE OR DETERIORATION TO MATERIALS AND COMPONENTS
-CONDITIONS OF INSTABILITY OR LACK OF SUPPORT
-ITEMS NOTED AS EXISTING ON THE DRAWINGS BUT NOT FOUND IN THE FIELD

3C) PREPARE DIMENSIONAL DRAWINGS OF ALL DISCOVERED ITEMS.

3D) CONTRACTOR SHALL FIELD VERIFY ALL EXISTING STRUCTURAL CONDITIONS PRIOR TO SUBMITTING SHOP DRAWINGS.

3E) CONTRACTOR SHALL MAKE ALLOWANCE FOR THE RESOLUTION OF SUCH DISCOVERIES IN THE CONSTRUCTION SCHEDULE.

3F) SUBMIT A DIMENSIONED DRAWING OF ALL NEW OPENINGS THROUGH EXISTING STRUCTURE AND SECURE APPROVAL PRIOR TO CUTTING. NEW OPENING MAY BE EITHER SHOWN ON THE CONTRACT DOCUMENTS OR PROPOSED BY THE CONTRACTOR. DRAWING SHALL SHOW:
- VERTICAL & HORIZONTAL LOCATION AND SIZE OF NEW OPENING(S)
-ALL EXISTING OPENINGS IN THE VICINITY OF THE NEW OPENING(S)
-ALL EXISTING STRUCTURE (BEAMS, COLUMNS, SLABS, WALLS, ETC) IN THE VICINITY OF THE NEW OPENING(S)
-ALL REINFORCING BAR SIZES AND POSITIONS (LAYOUT LOCATION AND DEPTH) CONFLICTING WITH OR IN THE VICINITY OF THE NEW OPENING(S).

4) SUBMITTALS AND SUBSTITUTIONS:

4A) SUBMITTALS:
- 042010 - REINFORCED UNIT MASONRY
  - PRODUCT DATA FOR MASONRY BLOCK, REBAR, ANCHOR BOLTS.
  - MIX DESIGNS FOR MORTAR AND GROUT
  - SHOP DRAWINGS FOR REINFORCING STEEL THAT COMPLY WITH ACI 315, "DETAILS AND DETAILING OF CONCRETE REINFORCMENT". SHOW ELEVATIONS OF REINFORCED WALLS. DRAWINGS SHALL INCLUDE:
    - 1/4" SCALE ELEVATIONS OF ALL WALLS WITH OPENINGS AND REINFORCING SHOWN
    - TOP AND BOTTOM ELEVATIONS OF WALLS AND BEARING ELEVATIONS OF ALL ELEMENTS SUPPORTED.
    - SIZE AND LOCATION OF ALL OPENINGS, EMBEDMENTS AND ANCHOR BOLTS.
    - BAR SIZES, LOCATION AND QUANTITIES OF REINFORCING STEEL.
    - ALL CONTROL JOINTS

-IF THE CONTRACTOR REQUESTS A CHANGE FROM THE STRUCTURAL DRAWINGS, IT SHALL BE APPROVED BY AND DESIGNED BY MARTIN/MARTIN, INC. PRIOR TO SUBMITTING SHOP DRAWINGS. VARIATION SHALL BE INDICATED ON THE SHOP DRAWINGS. CONTRACTOR SHALL COMPENSATE MARTIN/MARTIN, INC. FOR MAKING THE CHANGE.
-CONSTRUCTION DOCUMENTS SHALL NOT BE REPRODUCED FOR USE IN SUBMITTALS
-ALL SHOP DRAWINGS SHALL REFERENCE THE STRUCTURAL DRAWING NUMBER AND DETAIL USED TO PREPARE THE SUBMITTAL

4B) SUBSTITUTIONS: ENGINEER'S APPROVAL SHALL BE SECURED FOR ALL SUBSTITUTIONS

4C) NONCONFORMANCE: NOTIFY ENGINEER OF CONDITIONS NOT CONSTRUCTED PER THE CONTRACT DOCUMENTS PRIOR TO PROCEEDING WITH CORRECTIVE WORK. SUBMIT PROPOSED REPAIR TO THE ENGINEER FOR ACCEPTANCE. CONTRACTOR SHALL COMPENSATE MARTIN/MARTIN, INC. FOR DESIGNING THE REPAIR.

4D) ALL SHOP DRAWINGS SHALL BE SUBMITTED IN ELECTRONIC FORMAT ONLY.

5) TEMPORARY CONDITIONS, CONSTRUCTION ENGINEERING, AND OSHA STANDARDS:

5A) THE STRUCTURE IS DESIGNED TO FUNCTION AS A UNIT UPON COMPLETION AND ONLY FOR LOADS ANTICIPATED DURING THE STRUCTURE'S SERVICE LIFE.

5B) THE CONTRACTOR IS RESPONSIBLE FOR FURNISHING ALL TEMPORARY BRACING AND/OR SUPPORT THAT MAY BE REQUIRED AS THE RESULT OF THE CONTRACTOR'S CONSTRUCTION METHODS AND/OR SEQUENCES. CONTRACTOR SHALL PROVIDE ALL REQUIRED ENGINEERING AND OTHER MEASURES TO ACHIEVE THE MEANS, METHODS, AND SEQUENCES OF WORK WHICH MAY INCLUDE, BUT IS NOT LIMITED TO:
-LAYOUT
-DESIGN FOR FORMWORK, SHORING, AND RESHORING
-DESIGN OF CONCRETE MIXES
-DESIGN OF TEMPORARY BRACING OF WALLS FOR WIND, OR SEISMIC LOADS
-SURVEYING TO VERIFY CONSTRUCTION TOLERANCES
-STRUCTURAL ENGINEERING TO RESIST ANY OTHER LOADS NOT IDENTIFIED ON DESIGN DRAWINGS

5C) NOTHING SHOWN ON THE STRUCTURAL DRAWINGS SHALL BE CONSTRUED AS ELIMINATING THE NEED FOR THE CONTRACTOR TO COMPLY WITH ALL OSHA REQUIREMENTS. WHERE THE STRUCTURAL DRAWINGS APPEAR TO CONFLICT WITH OSHA REQUIREMENTS, THE STRUCTURAL DRAWINGS REPRESENT FINAL CONDITIONS ONLY.

MARTIN/MARTIN CONSULTING ENGINEERS
12499 WEST COLFAX AVENUE, LAKEWOOD, COLORADO 80215
MAIN 303.431.6100 MARTINMARTIN.COM



SPRING CREEK PARK / PAVILION VEHICLE STRIKE REPAIR

4001 SOUTH HIMALAYA STREET AURORA, COLORADO 80013

REVISIONS

NO.	ISSUE	DATE
1	FOR CONSTRUCTION	09/16/2026

PROJECT NO: 26.1101.S.01
DATE: 09/16/2026

© MARTIN/MARTIN 2025

SHEET TITLE: GENERAL NOTES

SHEET NUMBER: S0.1

Martin/Martin, Inc. retains the design rights to this Plan or other printed material. All rights are reserved. Unauthorized use of this material, particularly the alteration of any dimension or detail shown, the deletion of any part of this Plan, the separation of sheets from the original bound set, or the incorporation of this material in any other plan or document without the permission of Martin/Martin, Inc. constitutes misappropriation of its copyright and other rights. The recipient agrees to indemnify and hold harmless Martin/Martin, Inc. from any claims, damages, losses, expenses, or liabilities arising out of the recipient's unauthorized use of this material. Submission or distribution of this material to meet official regulatory requirements or for similar purposes in connection with the project is not to be construed as publication in derogation of Martin/Martin, Inc.'s reserved rights.

MM_JOB #: 26.1101.S.01
PRINCIPAL: NICOLE LANE
EOR: LUKE WALDO
PROJECT MANAGER: GREG RADEMACHER

DESIGNERS: GREG RADEMACHER
LEAD REVIT TECH: YASEMIN AYHAN
DATE PRINTED: 9/16/2026 8:37:14 AM
FILE PATH: Autodesk Docs://ACC-MM S26\26.1101.S.01-Spring Creek Park - Pavilion Vehicle Strike-S26.rvt

SPECIAL INSPECTIONS AND TESTING

JOBSITE TESTING AND INSPECTION REQUIREMENTS - GENERAL

A.GENERAL:
1.SCOPE OF WORK
A.THE OWNER WILL ENGAGE A QUALIFIED INSPECTION AND TESTING AGENCY(S) TO PERFORM SPECIAL INSPECTIONS AND TESTING FOR ALL STRUCTURAL MEMBERS AND ASSEMBLIES AS NOTED HEREIN.
B.SPECIAL INSPECTIONS ARE IN ADDITION TO INSPECTIONS BY THE AUTHORITY HAVING JURISDICTION REQUIRED BY IBC 2024 SECTION 110.

2.SPECIAL INSPECTIONS AND TESTING ARE APPLICABLE TO ALL REVISIONS AND/OR FUTURE WORK ADDED BY AMENDMENTS TO THE CONSTRUCTION DOCUMENTS.

3.DEFINITIONS
A.SPECIAL INSPECTOR: THE AGENCY ENGAGED BY THE OWNER AND APPROVED BY THE AUTHORITY HAVING JURISDICTION TO ACT AS THE DESIGNATED REPRESENTATIVE TO PERFORM INSPECTIONS.
B.SPECIAL INSPECTION: INSPECTION PERFORMED BY THE SPECIAL INSPECTOR ACCORDING TO IBC 2024 SECTION 1704 TO ENSURE COMPLIANCE WITH APPROVED CONSTRUCTION DOCUMENTS AND REFERENCED STANDARDS.
C.(P) PERIODIC INSPECTION: THE PART-TIME OR INTERMITTENT OBSERVATION BY THE SPECIAL INSPECTOR OF WORK BEING PERFORMED. SPECIAL INSPECTOR SHALL BE PRESENT IN THE AREA WHERE THE WORK IS BEING PERFORMED. OBSERVATION OF ALL WORK (100% VISUAL) SHALL BE MADE AT THE COMPLETION OF THE WORK.
D.(C) CONTINUOUS INSPECTION: THE FULL-TIME OBSERVATION BY THE SPECIAL INSPECTOR OF WORK BEING PERFORMED. SPECIAL INSPECTOR SHALL BE PRESENT IN THE AREA WHERE THE WORK IS BEING PERFORMED. OBSERVATION OF ALL WORK (100% VISUAL) SHALL BE MADE AT THE COMPLETION OF THE WORK.
E.(100%): 100% OBSERVATION / TESTING PRIOR TO CONCEALMENT OF INDICATED ELEMENT.
F.TESTING AND INSPECTION TYPE 1: MATERIAL VERIFICATION AND WORKMAN CERTIFICATIONS.
G.TESTING AND INSPECTION TYPE 2: SITE INSPECTION FOR LAYOUT AND QUANTITIES.
H.TESTING AND INSPECTION TYPE 3: SITE INSPECTION FOR PROCEDURES AND WORKMANSHIP.
I.TESTING AND INSPECTION TYPE 4: SITE TESTING FOR MATERIAL PROPERTIES AND WORKMANSHIP.

4.DEFICIENCIES IN WORK
A.CORRECT DEFICIENCIES IN WORK THAT TESTS AND INSPECTIONS INDICATE DO NOT COMPLY WITH THE CONTRACT DOCUMENTS AND REFERENCED STANDARDS.
B.ALL COST OF ADDITIONAL TESTING AND/OR INSPECTIONS FOR CORRECTIVE WORK SHALL BE BORNE BY THE CONTRACTOR.

JOBSITE TESTING AND INSPECTION REQUIREMENTS FOR MASONRY – LEVEL 2 (RISK CATEGORY I, II, OR III)

A.GENERAL
1.COMPLIANCE WITH APPROVED SUBMITTALS.
A.TYPE 2: SITE INSPECTION FOR LAYOUT AND QUANTITIES.
B.CRITERIA: VERIFY COMPLIANCE WITH APPROVED SUBMITTALS.
C.FREQUENCY: (P) PERIODIC INSPECTION.
D.STANDARD: TMS 602, ART 1.5.

B.AS MASONRY CONSTRUCTION BEGINS
1.VERIFY F'M.
A.TYPE 1: MATERIAL VERIFICATION AND WORKMAN CERTIFICATIONS.
B.CRITERIA: VERIFY SPECIFIED COMPRESSIVE STRENGTH OF MASONRY, F'M CONFORMS TO STRUCTURAL DRAWINGS AND SPECIFICATIONS.
C.FREQUENCY: 100% OBSERVATION / TESTING.

2.PROPORTIONS OF SITE-PREPARED MORTAR.
A.TYPE 1: MATERIAL VERIFICATION AND WORKMAN CERTIFICATIONS.
B.CRITERIA: VERIFY PROPORTIONS OF SITE-PREPARED MORTAR CONFORM TO STANDARD.
C.FREQUENCY: (P) PERIODIC INSPECTION.
D.STANDARD: TMS 602, ART 2.1 AND 2.6A.

3.CONSTRUCTION OF MORTAR JOINTS.
A.TYPE 3: SITE INSPECTION FOR PROCEDURES AND WORKMANSHIP.
B.CRITERIA: VERIFY CONSTRUCTION OF MORTAR JOINTS CONFORMS TO STANDARD.
C.FREQUENCY: (P) PERIODIC INSPECTION.
D.STANDARD: TMS 602, ART. 3.3B.

4.REINFORCEMENT, ANCHORAGES, CONNECTORS, EMBEDS.
A.TYPE 2: SITE INSPECTION FOR LAYOUT AND QUANTITIES.
B.CRITERIA: GRADE, TYPE, AND SIZE OF REINFORCEMENT, CONNECTORS, ANCHOR BOLTS.
C.FREQUENCY: (P) PERIODIC INSPECTION.
D.STANDARD: TMS602, ART 3.4.

5.SAMPLE PANEL CONSTRUCTION
A.TYPE 3: SITE INSPECTION FOR PROCEDURES AND WORKMANSHIP.
B.CRITERIA: USE OF MATERIALS AND PROCEDURES ACCEPTED FOR THE WORK. MINIMUM PANEL DIMENSIONS ARE 4 FEET BY 4 FEET. THE ACCEPTABLE STANDARD FOR THE WORK IS ESTABLISHED BY THE ACCEPTED PANEL.
C.FREQUENCY: (P) PERIODIC INSPECTION.
D.STANDARD: TMS 602, ART 1.6D.

C.DURING CONSTRUCTION
1.PLACEMENT OF MASONRY UNITS AND MORTAR JOINT CONSTRUCTION.
A.TYPE 2: SITE INSPECTION FOR LAYOUT AND QUANTITIES.
B.CRITERIA: VERIFY PLACEMENT OF MASONRY UNITS AND MORTAR JOINT CONSTRUCTION IS IN COMPLIANCE WITH THE STANDARD.
C.FREQUENCY: (P) PERIODIC INSPECTION.
D.STANDARD: TMS 602, ART. 3.3B.

2.SIZE AND LOCATION OF ELEMENTS.
A.TYPE 2: SITE INSPECTION FOR LAYOUT AND QUANTITIES.
B.CRITERIA: VERIFY SIZE AND LOCATION OF STRUCTURAL ELEMENTS CONFORMS TO DRAWINGS AND SPECIFICATIONS.
C.FREQUENCY: (P) PERIODIC INSPECTION.
D.STANDARD: TMS 602, ART. 3.3F.

3.TYPE, SIZE AND LOCATION REINFORCEMENT AND EMBEDS.
A.TYPE 2: MATERIAL VERIFICATION AND WORKMAN CERTIFICATIONS.
B.CRITERIA: VERIFY TYPE, SIZE, AND LOCATION OF ANCHORS, INCLUDING OTHER DETAILS OF ANCHORAGE OF MASONRY TO STRUCTURAL MEMBERS, FRAMES, OR OTHER CONSTRUCTIONS.
C.FREQUENCY: (P) PERIODIC INSPECTION.

4.COLD (<40F) AND HOT (>90F) WEATHER.
A.TYPE 3: SITE INSPECTION FOR PROCEDURES AND WORKMANSHIP.
B.CRITERIA: VERIFY PREPARATION, CONSTRUCTION, AND PROTECTION OF MASONRY DURING HOT AND COLD WEATHER CONFORM TO STANDARD.
C.FREQUENCY: (P) PERIODIC INSPECTION.
D.STANDARD: TMS 602, ART. 1.8C AND 1.8D.

D.PRIOR TO GROUTING
1.GROUT SPACE.
A.TYPE 3: SITE INSPECTION FOR PROCEDURES AND WORKMANSHIP.
B.CRITERIA: VERIFY GROUT SPACE IS FREE OF MORTAR DROPPINGS AND DEBRIS, AND CLEANOUTS PROVIDED AS REQUIRED.
C.FREQUENCY: (P) PERIODIC INSPECTION.
D.STANDARD: TMS 602, ART. 3.2D AND 3.2F.

2.REINFORCEMENT, ANCHORAGES, CONNECTORS, EMBEDS.
A.TYPE 2: SITE INSPECTION FOR LAYOUT AND QUANTITIES.
B.CRITERIA: VERIFY TYPE, SIZE, QUANTITY, LOCATION, SPACING, COVER, SPLICE LENGTH, SPLICE LOCATION, SURFACE CONDITION, SUPPORT, AND SECURING. SEE STRUCTURAL CONCRETE TABLE AND SPECIFICATIONS FOR FIELD BENDING, COATED REINFORCEMENT, AND MECHANICAL CONNECTORS.
C.FREQUENCY: (P) PERIODIC INSPECTION, 100% OBSERVATION/TESTING.
D.STANDARD: TMS602, ART. 2.4 AND 3.4, STRUCTURAL CONCRETE TABLE AND SPECIFICATIONS.

3.PROPORTIONS OF SITE MIXED GROUT.
A.TYPE 1: MATERIAL VERIFICATION AND WORKMAN CERTIFICATIONS.
B.CRITERIA: VERIFY PROPORTIONS OF SITE MIXED GROUT CONFORM TO ASTM C476.
C.FREQUENCY: (P) PERIODIC INSPECTION.
D.STANDARD: TMS 602, ART. 2.6B, ASTM C476.

4.MIX DESIGN FOR OFF-SITE PREPARED GROUT.
A.TYPE 1: MATERIAL VERIFICATION AND WORKMAN CERTIFICATIONS.
B.CRITERIA: VERIFY MIX DESIGN FOR OFF-SITE PREPARED GROUT CONFORMS TO STANDARD.
C.FREQUENCY: 100% OBSERVATION / TESTING.
D.STANDARD: TMS 602, ART. 2.6B, ASTM C476.

5.CONSTRUCTION OF MORTAR JOINTS.
A.TYPE 3: SITE INSPECTION FOR PROCEDURES AND WORKMANSHIP.
B.CRITERIA: VERIFY CONSTRUCTION OF MORTAR JOINTS CONFORMS TO STANDARD.
C.FREQUENCY: (P) PERIODIC INSPECTION.
D.STANDARD: TMS 602, ART. 3.3B.

JOBSITE TESTING & INSPECTION REQUIREMENTS - GENERAL

Inspection / Testing General Notes:

1. Special inspections & testing indicated in the attached tables will be completed by the Owner's 3rd party testing & inspection agency.
2. Contractor shall request and coordinate testing & inspection activities with the 3rd party agency to meet the requirements of the attached tables, notes and specifications.
3. See notes for additional information and requirements of each inspection / test.

TESTING & INSPECTION TYPES	
1	Material Verification & Workman Certifications
2	Site Inspection for Layout & Quantities
3	Site Inspection for Procedures & Workmanship
4	Site Testing for Material Properties & Workmanship
TESTING & INSPECTION FREQUENCY DEFINITIONS	
C	Continuous Inspection - Full-time observation by the special inspector of the work being performed.
P	Periodic Inspection - The part-time or intermittent observation by the special inspector of the work being performed. 100% visual observation of all work at the completion of the work.
##%	##% observation / testing prior to concealment of indicated element

JOBSITE TESTING & INSPECTION REQUIREMENTS - MASONRY

Testing / Inspection Type	1	2	3	4	5
STRUCTURAL MASONRY INSPECTIONS - LEVEL 2 (RISK CATEGORY I, II OR III)					
Compliance with Approved Submittals		P			
Observe Preparation of Grout, Mortar			P		
As Masonry Construction Begins					
Verify f'm	100%				
Proportions of Site-prepared Mortar	P				
Construction of Mortar Joints			P		
Reinforcing, Anchorages, Connectors, Embedments		P			
During Construction					
Size & Location of Elements		P			
Placement of Masonry Units and Mortar Joint Construction		P			
Type, Size & Location Reinf & Embeds		P			
Cold (<40F) & Hot (>90F) Weather			P		
Placement of Grout			C		
Prior to Grouting					
Grout space			P		
Reinf, Anchorages, Connectors, Embeds	P	100%			
Proportions of Site Mixed Grout	P				
Mix Design for Off-Site Prepared Grout	100%				
Construction of Mortar Joints			P		

MARTIN/MARTIN CONSULTING ENGINEERS
12499 WEST COLFAX AVENUE, LAKEWOOD, COLORADO 80215
MAIN 303.431.6100 MARTINMARTIN.COM



SPRING CREEK PARK / PAVILION VEHICLE STRIKE REPAIR

4001 SOUTH HIMALAYA STREET AURORA, COLORADO 80013

REVISIONS

NO.	ISSUE	DATE
1	FOR CONSTRUCTION	09/16/2026

PROJECT NO: 26.1101.S.01
DATE: 09/16/2026

© MARTIN/MARTIN 2025


SHEET TITLE:
SPECIAL INSPECTIONS

SHEET NUMBER:
S0.2

Any drawing, text, computer model, design, concept, or other work prepared by Martin/Martin, whether in hard copy or electronic form, is an instrument of service and shall remain the property of Martin/Martin. Martin/Martin shall retain all common law, statutory and other reserved rights, including the copyright thereto. Any use of these documents, in whole or in part, without the written permission of Martin/Martin is prohibited. Martin/Martin shall not be liable for any modifications made to these documents without the written approval of Martin/Martin. Any unauthorized use of these documents shall be at the sole risk of the user, and the user agrees to defend, indemnify and hold harmless Martin/Martin from all claims, damages, losses and expenses, including attorneys' fees, arising out of or resulting from such use. Submission or distribution of these documents to meet official regulatory requirements or for similar purposes in connection with the project is not to be construed as publication in derogation of Martin/Martin's reserved rights.

MM JOB #: 26.1101.S.01
PRINCIPAL: NICOLE LANE
EOR: LUKE WALDO
PROJECT MANAGER: GREG RADEMACHER

DESIGNERS: GREG RADEMACHER
LEAD REVIT TECH: YASEMIN AYHAN
DATE PRINTED: 9/16/2026 8:37:15 AM
FILE PATH: Autodesk Docs://ACC-MM S26\26.1101.S.01-Spring Creek Park - Pavilion Vehicle Strike-S26.rvt

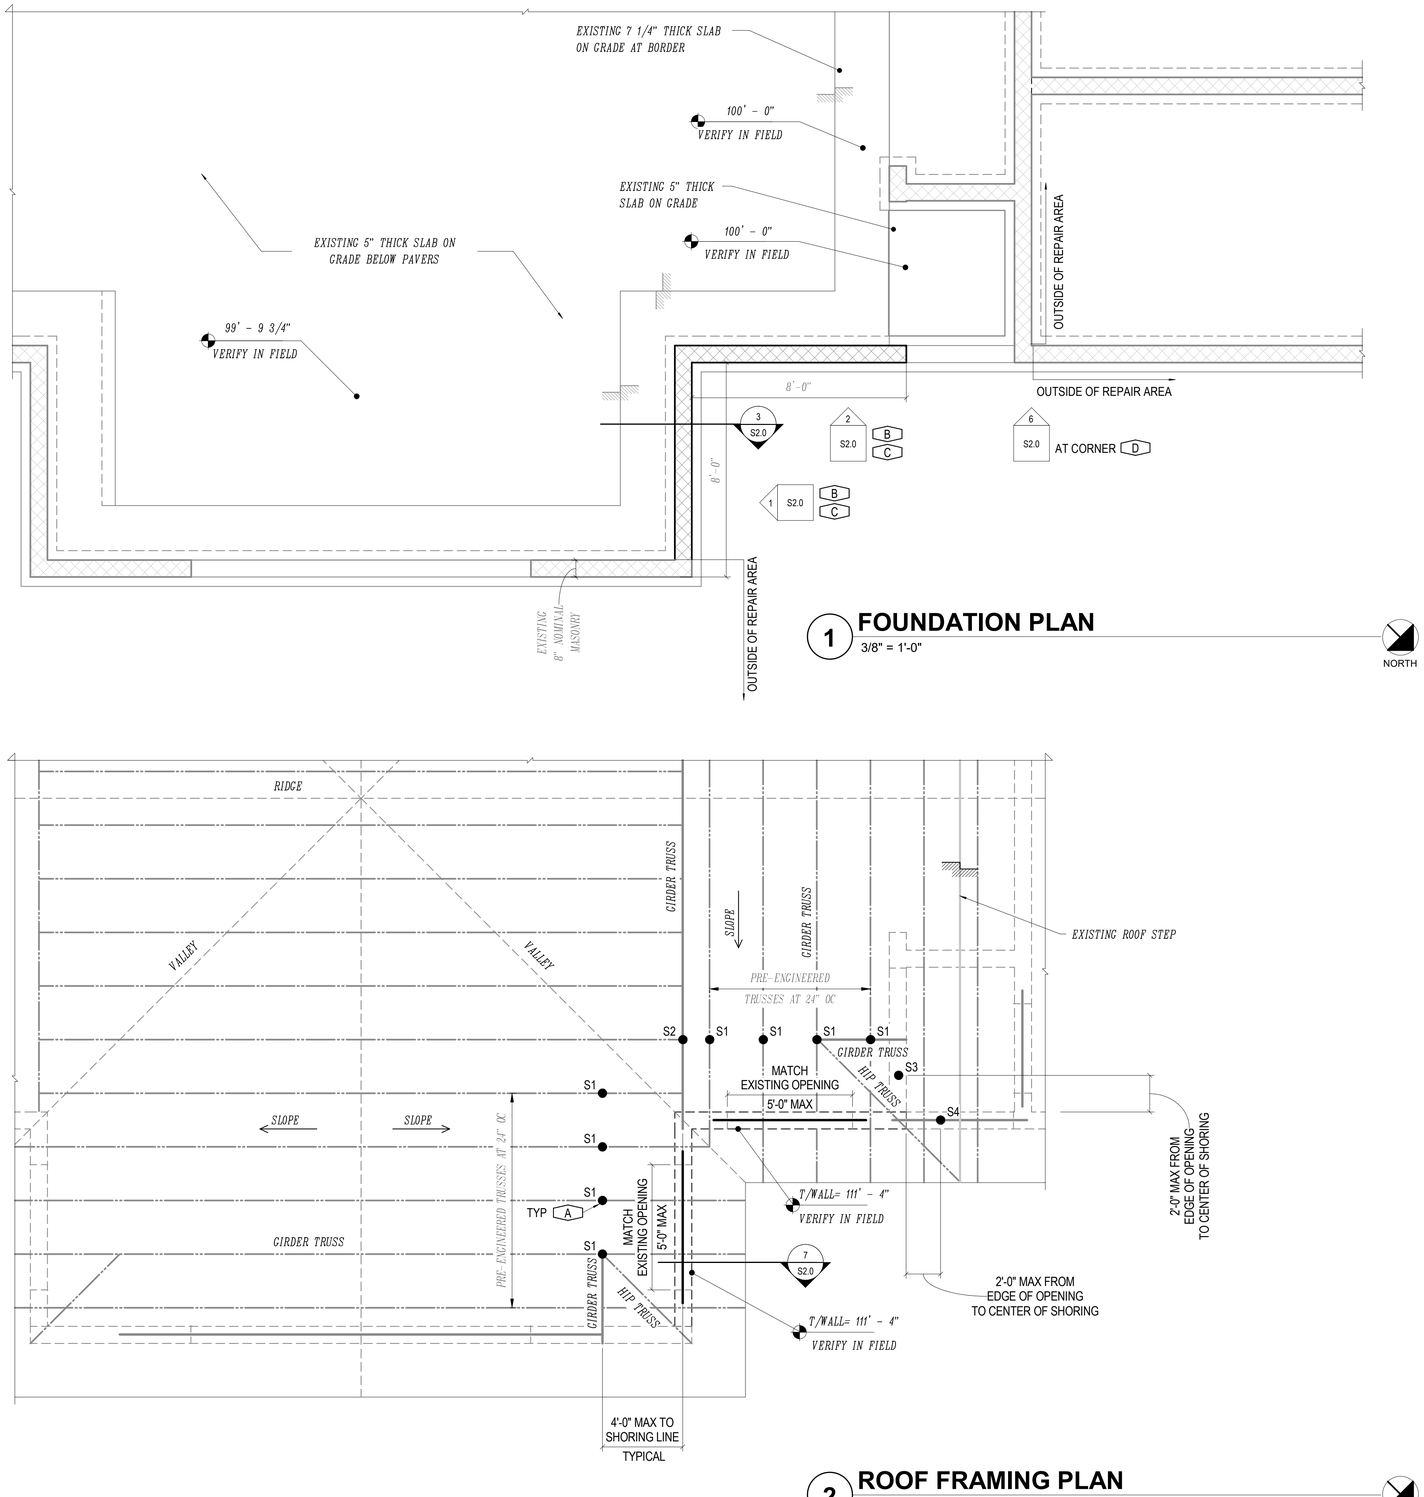

1 FOUNDATION PLAN
3/8" = 1'-0"

NORTH

2 ROOF FRAMING PLAN
3/8" = 1'-0"


NORTH

STRUCTURAL WORK LIST KEYNOTES

DESCRIPTION	WORK ITEM	ESTIMATED QUANTITY
SHORE EXISTING ROOF. SHORING DESIGN BY CONTRACTOR SHORING ENGINEER. SEE SHORING DESIGN LOADS TABLE	A	SEE SHORING NOTES
DEMOLISH EXISTING DAMAGED MASONRY WALLS.	B	SEE DETAILS
INSTALL REPLACEMENT MASONRY WALLS (INCLUDING STEEL LINTELS, ANCHOR BOLTS, AND POST-INSTALLED DOWELS).	C	SEE DETAILS
REPAIR DAMAGED EXISTING MASONRY UNITS TO REMAIN	D	SEE DETAILS

SHORING DESIGN LOADS

MARK	VERTICAL LOADING, KIPS (ALLOWABLE, ASD)	REMARKS
S1	DOWN LOAD = 1.8 NET UPLIFT LOAD = 0.55	SEE 7/S2.0
S2	DOWN LOAD = 11 NET UPLIFT LOAD = 3.3	SEE 7/S2.0
S3	DOWN LOAD = 1.35 NET UPLIFT LOAD = N/A	BELOW EXISTING STEEL LINTEL TO REMAIN
S4	DOWN LOAD = 2.5 NET UPLIFT LOAD = N/A	BELOW EXISTING STEEL LINTEL TO REMAIN



NORTH

KEY PLAN
NO SCALE

MARTIN/MARTIN CONSULTING ENGINEERS
12499 WEST COLFAX AVENUE, LAKEWOOD, COLORADO 80215
MAIN 303.431.6100 MARTINMARTIN.COM



SPRING CREEK PARK / PAVILION VEHICLE STRIKE REPAIR

4001 SOUTH HIMALAYA STREET AURORA, COLORADO 80013

REVISIONS

NO.	ISSUE	DATE
1	FOR CONSTRUCTION	09/16/2026

PROJECT NO: 26.1101.S.01
DATE: 09/16/2026


© MARTIN/MARTIN 2025

SHEET TITLE: PARTIAL PLANS

SHEET NUMBER: S1.0

MM_JOB #: 26.1101.S.01
PRINCIPAL: NICOLE LANE
EOR: LUKE WALDO
PROJECT MANAGER: GREG RADEMACHER


DESIGNERS: GREG RADEMACHER
LEAD REVIT TECH: YASEMIN AYHAN
DATE PRINTED: 9/16/2026 8:37:15 AM
FILE PATH: Autodesk Docs://ACC-MM S26\26.1101.S.01-Spring Creek Park - Pavilion Vehicle Strike-S26.rvt

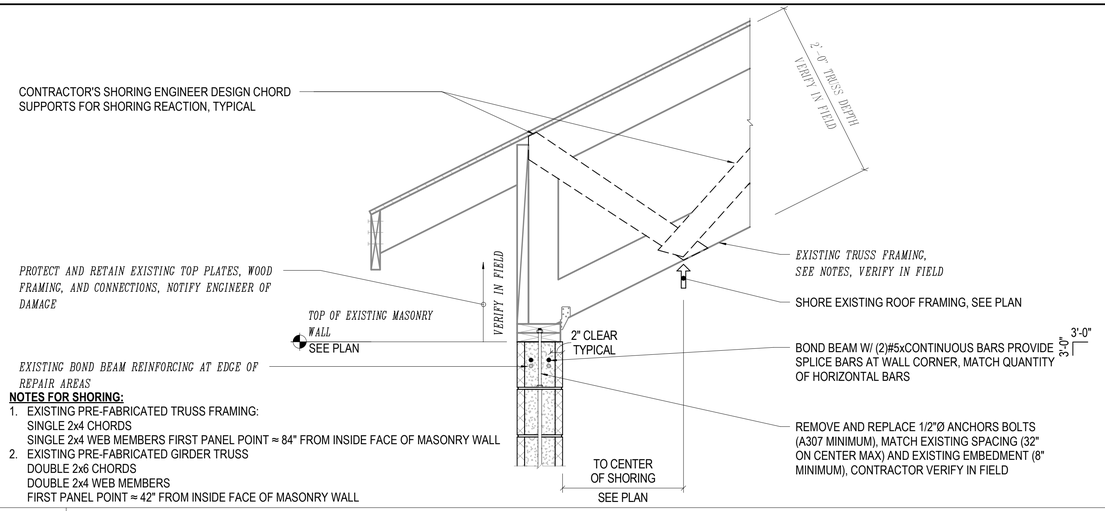


NOTES FOR SHORING:

1. EXISTING PRE-FABRICATED TRUSS FRAMING:
   SINGLE 2x4 CHORDS
   SINGLE 2x4 WEB MEMBERS FIRST PANEL POINT ≈ 84" FROM INSIDE FACE OF MASONRY WALL
2. EXISTING PRE-FABRICATED GIRDER TRUSS
   DOUBLE 2x6 CHORDS
   DOUBLE 2x4 WEB MEMBERS
   FIRST PANEL POINT ≈ 42" FROM INSIDE FACE OF MASONRY WALL


7 1" = 1'-0" TYPICAL TRUSS BEARING DETAIL

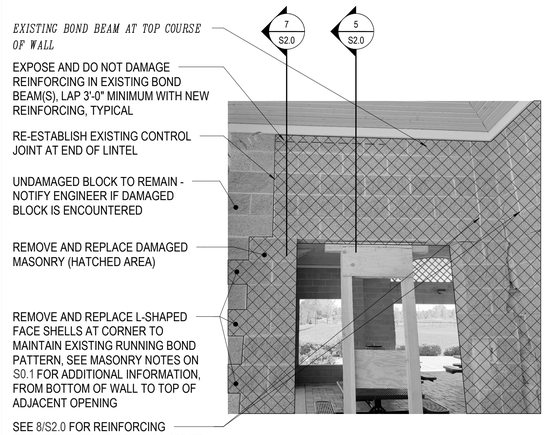


1 NO SCALE NORTH WALL REPAIR



8 1 1/2" = 1'-0" TYPICAL MASONRY WALL CONTROL JOINT

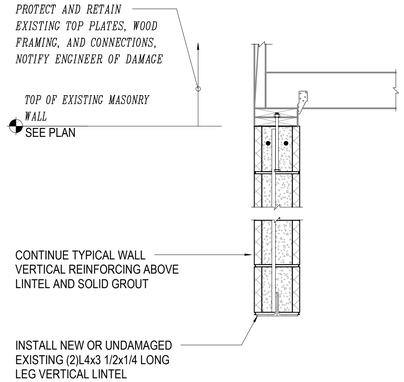


5 1" = 1'-0" LOOSE LINTEL ABOVE OPENING IN WALL

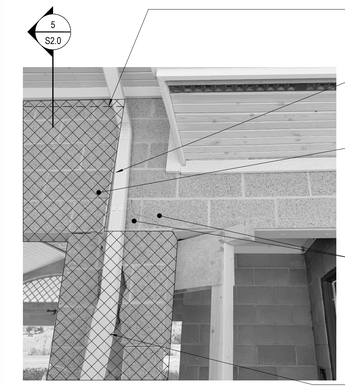

NOTES:

1. SEE MASONRY NOTES ON S0.1 FOR ADDITIONAL INFORMATION.
2. SEE 1/S2.0 FOR ADDITIONAL INFORMATION SHOWN BUT NOT NOTED


2 NO SCALE EAST WALL REPAIR

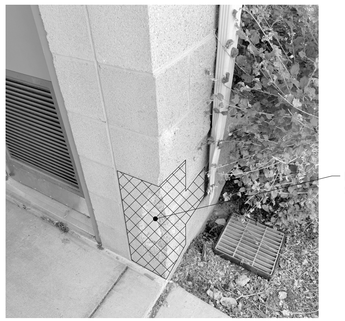

NOTES:

1. SEE MASONRY NOTES ON S0.1 FOR ADDITIONAL INFORMATION.

6 NO SCALE ELEAVTION AT CORNER

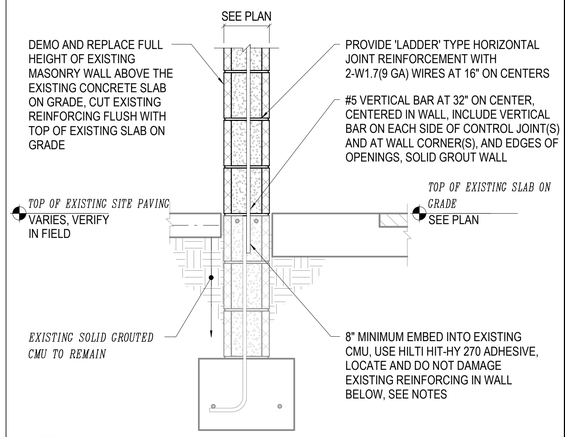

NOTES:

1. CONTRACTOR TO SUBMIT PHOTO DOCUMENTATION TO THE ENGINEER OF THE EXISTING MASONRY WALL TO REMAIN BELOW GRADE FOR EVALUATION PRIOR TO INSTALLING ADHESIVE DOWELS.

3 1" = 1'-0" FOUNDATION DETAIL

MARTIN/MARTIN CONSULTING ENGINEERS
12499 WEST COLFAX AVENUE, LAKEWOOD, COLORADO 80215
MAIN 303.431.6100 MARTINMARTIN.COM



SPRING CREEK PARK / PAVILION VEHICLE STRIKE REPAIR

4001 SOUTH HIMALAYA STREET AURORA, COLORADO 80013

REVISIONS

NO.	ISSUE	DATE
1	FOR CONSTRUCTION	09/16/2026

PROJECT NO: 26.1101.S.01
DATE: 09/16/2026

© MARTINMARTIN 2025

SHEET TITLE: DETAILS

SHEET NUMBER: S2.0

MM JOB #: 26.1101.S.01
PRINCIPAL: NICOLE LANE
EOR: LUKE WALDO
PROJECT MANAGER: GREG RADEMACHER

DESIGNERS: GREG RADEMACHER
LEAD REVIT TECH: YASEMIN AYHAN
DATE PRINTED: 9/16/2026 8:37:17 AM
FILE PATH: Autodesk Docs://ACC-MM S26/26.1101.S.01-Spring Creek Park - Pavilion Vehicle Strike-S26.rvt

Engle Martin

5565 Glenridge Connector
Suite 900
Atlanta, GA 30342

Insured:	Trails Park and Recreation District
Property:	4001 S Himalaya Ave Aurora, CO 80013

Claim Rep.:	Wes Ellis	Business:	5565 Glenridge Connector, Suite 900 Atlanta, Georgia 30342
Position:	Executive General Adjuster	Business:	(843) 267-5216
Company:	Engle Martin	E-mail:	wellis@englemartin.com

Estimator:	Wes Ellis	Business:	(843) 267-5216
Position:	Executive General Adjuster	E-mail:	wellis@englemartin.com
Company:	Engle Martin		
Business:	5565 Glenridge Connector, Suite 900 Atlanta, Georgia 30342		

Claim Number: 4A2607MQ4GK-0001 **Policy Number:** NOT PROVIDED **Type of Loss:** Vehicle

Date Contacted:	7/30/2026 12:00 AM		
Date of Loss:	7/17/2026 12:00 AM	Date Received:	7/30/2026 12:00 AM
Date Inspected:	8/3/2026 12:00 AM	Date Entered:	7/30/2026 4:52 PM

Price List:	CODE8X_AUG26 Restoration/Service/Remodel
Estimate:	1000574928


VERY IMPORTANT! - PLEASE READ: This document is an initial estimate ONLY concerning the probable cost of repair of the damage. Additional inspection and/or investigation of the cause of loss and the damage related thereto may be required before this estimate can be finalized. Please note that this document is NOT a promise or agreement of payment for the claimed loss from the insurance company. We request that you present this estimate to your contractor for its review and comment. In the event of a scope of work or pricing discrepancy between this estimate and Your contractor's estimate, we will work with you and your contractor to attempt to resolve any differences. Finally, please note that You are responsible for selecting and hiring the contractor(s) that you want to perform your repair work. The insurance company does not guarantee the work of any contractor, nor do they inspect or monitor the work of any contractor. It is solely your responsibility to make sure that your repair work is properly and timely completed.

Engle Martin

5565 Glenridge Connector
Suite 900
Atlanta, GA 30342

1000574928

Interior



Pavilion **Height: Peaked**

2236.33	SF Walls	1350.70	SF Ceiling
3587.04	SF Walls & Ceiling	1345.94	SF Floor
149.55	SY Flooring	148.83	LF Floor Perimeter
160.90	LF Ceil. Perimeter		


Missing Wall	**6' X 14'**	**Opens into FRONT_ENTRAN**
Missing Wall	**5' 8" X 14'**	**Opens into BACK_ENTRANC**

DESCRIPTION	QTY
- Trash can	
1. Trash can	1.00 EA
2. General Laborer - per hour	1.00 HR
- Trash can installation	
- Flooring	
3. R&R Paver brick	196.00 SF
4. Mason - Brick / Stone - per hour	4.00 HR
- Extra labor to patch into the pre-existing floor.	
- Ceiling	
5. Remove Surveillance camera - color	4.00 EA
6. Install Surveillance camera - color	4.00 EA
7. Floor protection - plastic and tape - 10 mil	1345.94 SF
8. Mask more than the ceiling perimeter per square foot - plastic and tape - 4 mil	643.60 SF
9. Scissor lift - 20' platform height (per week)	2.00 WK
10. Equipment Operator - per hour	40.00 HR
11. Clean the ceiling	1350.70 SF
12. Stain & finish wood siding	1350.70 SF
13. R&R 1" x 6" lumber, Select pine (.5 BF per LF)	22.00 LF
14. Stain & finish trim	160.90 LF
15. Additional cost for high wall or ceiling - Over 14'	1350.70 SF
- Extra labor per ceiling design	
16. Painter - per hour	8.00 HR
- Cleaning	
17. Clean with pressure/chemical spray	2236.33 SF
18. Clean with pressure/chemical spray - Heavy	1345.94 SF

CONTINUED - Pavilion

DESCRIPTION	QTY
19. Final cleaning - construction - Commercial	1345.94 SF

NOTES:



Front Entrance **Height: 10'**

96.67	SF Walls	31.86	SF Ceiling
128.53	SF Walls & Ceiling	31.86	SF Floor
3.54	SY Flooring	8.67	LF Floor Perimeter
11.67	LF Ceil. Perimeter		


Door	**3' X 6' 8"**	**Opens into BATHROOM**
Missing Wall	**6' X 10'**	**Opens into PAVILION**
Missing Wall	**5' 2" X 10'**	**Opens into Exterior**

DESCRIPTION	QTY
- Ceiling	
20. R&R Recessed light fixture	1.00 EA
21. R&R 1" x 4" lumber (.333 BF per LF)	17.60 LF
22. R&R 5/8" drywall - hung, taped, heavy texture, ready for paint	31.86 SF
23. Floor protection - plastic and tape - 10 mil	31.86 SF
24. Mask more than the ceiling perimeter per square foot - plastic and tape - 4 mil	46.67 SF
25. Texture drywall - machine - knockdown	31.86 SF
26. Seal/prime (1 coat) then paint (2 coats) the ceiling	31.86 SF
- Cleaning	
27. Clean with pressure/chemical spray	128.53 SF
28. Final cleaning - construction - Commercial	31.86 SF

CONTINUED - Front Entrance

DESCRIPTION	QTY

NOTES:



Bathroom **Height: 10'**

490.00	SF Walls	152.00	SF Ceiling
642.00	SF Walls & Ceiling	152.00	SF Floor
16.89	SY Flooring	48.00	LF Floor Perimeter
51.00	LF Ceil. Perimeter		


Door **3' X 6' 8"** **Opens into FRONT_ENTRAN**

DESCRIPTION	QTY
- Door	
29. R&R Steel door, 3' x 7'	1.00 EA
30. R&R Door hinges (set of 3)	1.00 EA
31. Additional charge for a retrofit exterior door - difficult	1.00 EA
32. R&R Door lockset - exterior - High grade	1.00 EA
33. Paint door slab only - 2 coats (per side)	2.00 EA
34. Paint door/window trim & jamb - 2 coats (per side)	2.00 EA
- Hairline crack	
35. Masonry - Labor Minimum	1.00 EA
- hairline crack repair	
36. Clean masonry	152.00 SF
37. Floor protection - heavy paper and tape	64.00 SF
38. Mask and prep for paint - tape only (per LF)	51.00 LF
39. Seal brick with masonry sealer	152.00 SF
40. Paint brick	152.00 SF
- Cleaning	
41. Clean with pressure/chemical spray	152.00 SF

CONTINUED - Bathroom

DESCRIPTION	QTY
42. Final cleaning - construction - Commercial	152.00 SF

NOTES:

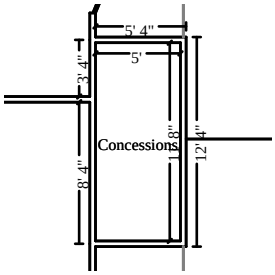


Concessions **Height: 10'**

333.33	SF Walls	58.33	SF Ceiling
391.67	SF Walls & Ceiling	58.33	SF Floor
6.48	SY Flooring	33.33	LF Floor Perimeter
33.33	LF Ceil. Perimeter		

DESCRIPTION	QTY
- Overhead door	
43. R&R Roll-up door & hardware - 10' x 10' - 22 gauge	1.00 EA
44. R&R Keyless entry pad for overhead door opener	1.00 EA
45. Paint overhead door - 2 coats (per side)	1.00 EA
- Cleaning	
46. Clean with pressure/chemical spray	58.33 SF
47. Final cleaning - construction - Commercial	58.33 SF

NOTES:

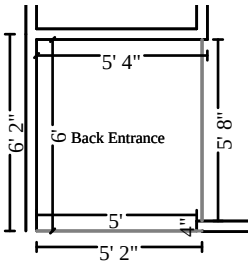

Back Entrance **Height: 10'**

116.22	SF Walls	30.83	SF Ceiling
147.06	SF Walls & Ceiling	30.83	SF Floor
3.43	SY Flooring	11.62	LF Floor Perimeter
11.62	LF Ceil. Perimeter		

Missing Wall	**5' X 10'**	**Opens into Exterior**
Missing Wall	**5' 8" X 10'**	**Opens into PAVILION**

DESCRIPTION	QTY
- Cleaning	
48. Clean with pressure/chemical spray	116.22 SF
49. Clean with pressure/chemical spray	30.83 SF
50. Final cleaning - construction - Commercial	30.83 SF

NOTES:

Exterior

Building


Building

DESCRIPTION	QTY
51. Remove Surveillance camera - color	4.00 EA
52. Install Surveillance camera - color	4.00 EA
- Gutter & downspout	
53. R&R Gutter / downspout - aluminum - up to 5"	60.00 LF
54. Prime & paint gutter / downspout	60.00 LF
- Fascia	
55. R&R Fascia - 1" x 6" - #1 pine	60.00 LF
56. Prime & paint exterior fascia - wood, 6"- 8" wide	60.00 LF
57. R&R Soffit - wood - tongue & groove	120.00 SF
58. R&R Soffit - box framing - 2' overhang	60.00 LF
59. Prime & paint exterior soffit - wood	120.00 SF
60. Soffit vent - linear	60.00 LF
- Masking	
61. Floor protection - plastic and tape - 10 mil	360.00 SF

CONTINUED - Building

DESCRIPTION	QTY
62. Mask and prep for paint - paper and tape (per LF)	150.00 LF

NOTES:




Framing — **Formula Elevation 30' x 12' x 0"**

297.74	SF Walls	30.00	LF Floor Perimeter
360.00	SF Long Wall	360.00	SF Short Wall
30.00	LF Ceil. Perimeter		

Missing Wall - Goes to neither Floor/Ceiling **4' 7" X 4' 7"** **Opens into Exterior**


Missing Wall - Goes to neither Floor/Ceiling **3' X 7'** **Opens into Exterior**



Subroom 1: offset — **Formula Elevation 9' x 12' x 0"**

87.75	SF Walls	9.00	LF Floor Perimeter
108.00	SF Long Wall	108.00	SF Short Wall
9.00	LF Ceil. Perimeter		

Missing Wall - Goes to neither Floor/Ceiling **4' 6" X 4' 6"** **Opens into Framing**



Subroom 2: Offset **Formula Elevation 6' x 12' x 0"**

72.00	SF Walls	6.00	LF Floor Perimeter
72.00	SF Long Wall	72.00	SF Short Wall
6.00	LF Ceil. Perimeter		

DESCRIPTION	QTY
- Bracing	
63. Temporary shoring post - Screw jack (per day)	112.00 DA
- Brick wall repairs	
64. Clean with pressure/chemical spray	457.49 SF
65. R&R Block - 8" x 8" x 16" - in place - reinforced	457.49 SF
66. Block - Add for scored or split faced block	457.49 SF
67. Join new brick to existing brick - per LF	24.00 LF
68. Mason - Brick / Stone - per hour	16.00 HR
- Additional labor to retrofit into the pre-existing wall.	

NOTES:

Sidewalk

DESCRIPTION	QTY
69. R&R Curb and Gutter - 24" - 30"	12.00 LF
70. Concrete grinding	250.00 SF
71. Concrete sidewalk - finished in place	75.00 SF
- Feather coating and blend	
72. Masonry acid wash	500.00 SF

NOTES:

Parking Lot

DESCRIPTION	QTY
73. Asphalt crack repair	200.00 LF

NOTES:

Street - Sidewalk

DESCRIPTION	QTY
74. R&R Curb and Gutter - 24" - 30"	12.00 LF
75. Concrete grinding	96.00 SF
76. Concrete sidewalk - finished in place	50.00 SF
- Feather coating and blen	
77. Masonry acid wash	200.00 SF

NOTES:

Landscapping

DESCRIPTION	QTY
- Pending estimate	

NOTES:

General Condition

DESCRIPTION	QTY
- Invoices	
78. Temporary Repairs (Bid Item)	2.00 EA
- NexGen Portables toilets due to the restrooms being out of use, estimating two monts from 2026-Jul-22 to 2026-Sep-22.	
- Temporary repairs	
79. Material Only 4" x 4" square wood post (1.33 BF per LF)	9.00 LF
80. Material Only Sheathing - plywood - 1/2" CDX	32.00 SF
81. Carpenter - General Framer - per hour	4.00 HR
82. Caution tape	800.00 LF
83. Traffic cones (per unit, per day)	600.00 DA
84. Emergency service call - after business hours	1.00 EA
85. Cleaning Technician - per hour	10.00 HR
- Supervision	
86. Commercial Supervision / Project Management - per hour	40.00 HR

NOTES:

Debris Removal

DESCRIPTION	QTY
87. Dumpster load - Approx. 20 yards, 4 tons of debris	1.00 EA
88. Tandem axle dump trailer - per load - including dump fees	1.00 EA

NOTES:

Labor Minimums Applied

DESCRIPTION	QTY
89. Finish hardware labor minimum	1.00 EA

CONTINUED - Labor Minimums Applied


DESCRIPTION	QTY
90. Drywall labor minimum	1.00 EA
91. Overhead door labor minimum	1.00 EA
92. Gutter labor minimum	1.00 EA

NOTES:

Grand Total Areas:

3,730.05	SF Walls	1,623.73	SF Ceiling	5,353.78	SF Walls and Ceiling
1,618.97	SF Floor	179.89	SY Flooring	295.46	LF Floor Perimeter
540.00	SF Long Wall	540.00	SF Short Wall	313.52	LF Ceil. Perimeter
1,618.97	Floor Area	1,694.41	Total Area	3,272.56	Interior Wall Area
2,777.91	Exterior Wall Area	205.64	Exterior Perimeter of Walls		
0.00	Surface Area	0.00	Number of Squares	0.00	Total Perimeter Length
0.00	Total Ridge Length	0.00	Total Hip Length		

VERY IMPORTANT! - PLEASE READ: This document is an initial estimate ONLY concerning the probable cost of repair of the damage. Additional inspection and/or investigation of the cause of loss and the damage related thereto may be required before this estimate can be finalized. Please note that this document is NOT a promise or agreement of payment for the claimed loss from the insurance company. We request that you present this estimate to your contractor for its review and comment. In the event of a scope of work or pricing discrepancy between this estimate and Your contractor's estimate, we will work with you and your contractor to attempt to resolve any differences. Finally, please note that You are responsible for selecting and hiring the contractor(s) that you want to perform your repair work. The insurance company does not guarantee the work of any contractor, nor do they inspect or monitor the work of any contractor. It is solely your responsibility to make sure that your repair work is properly and timely completed.

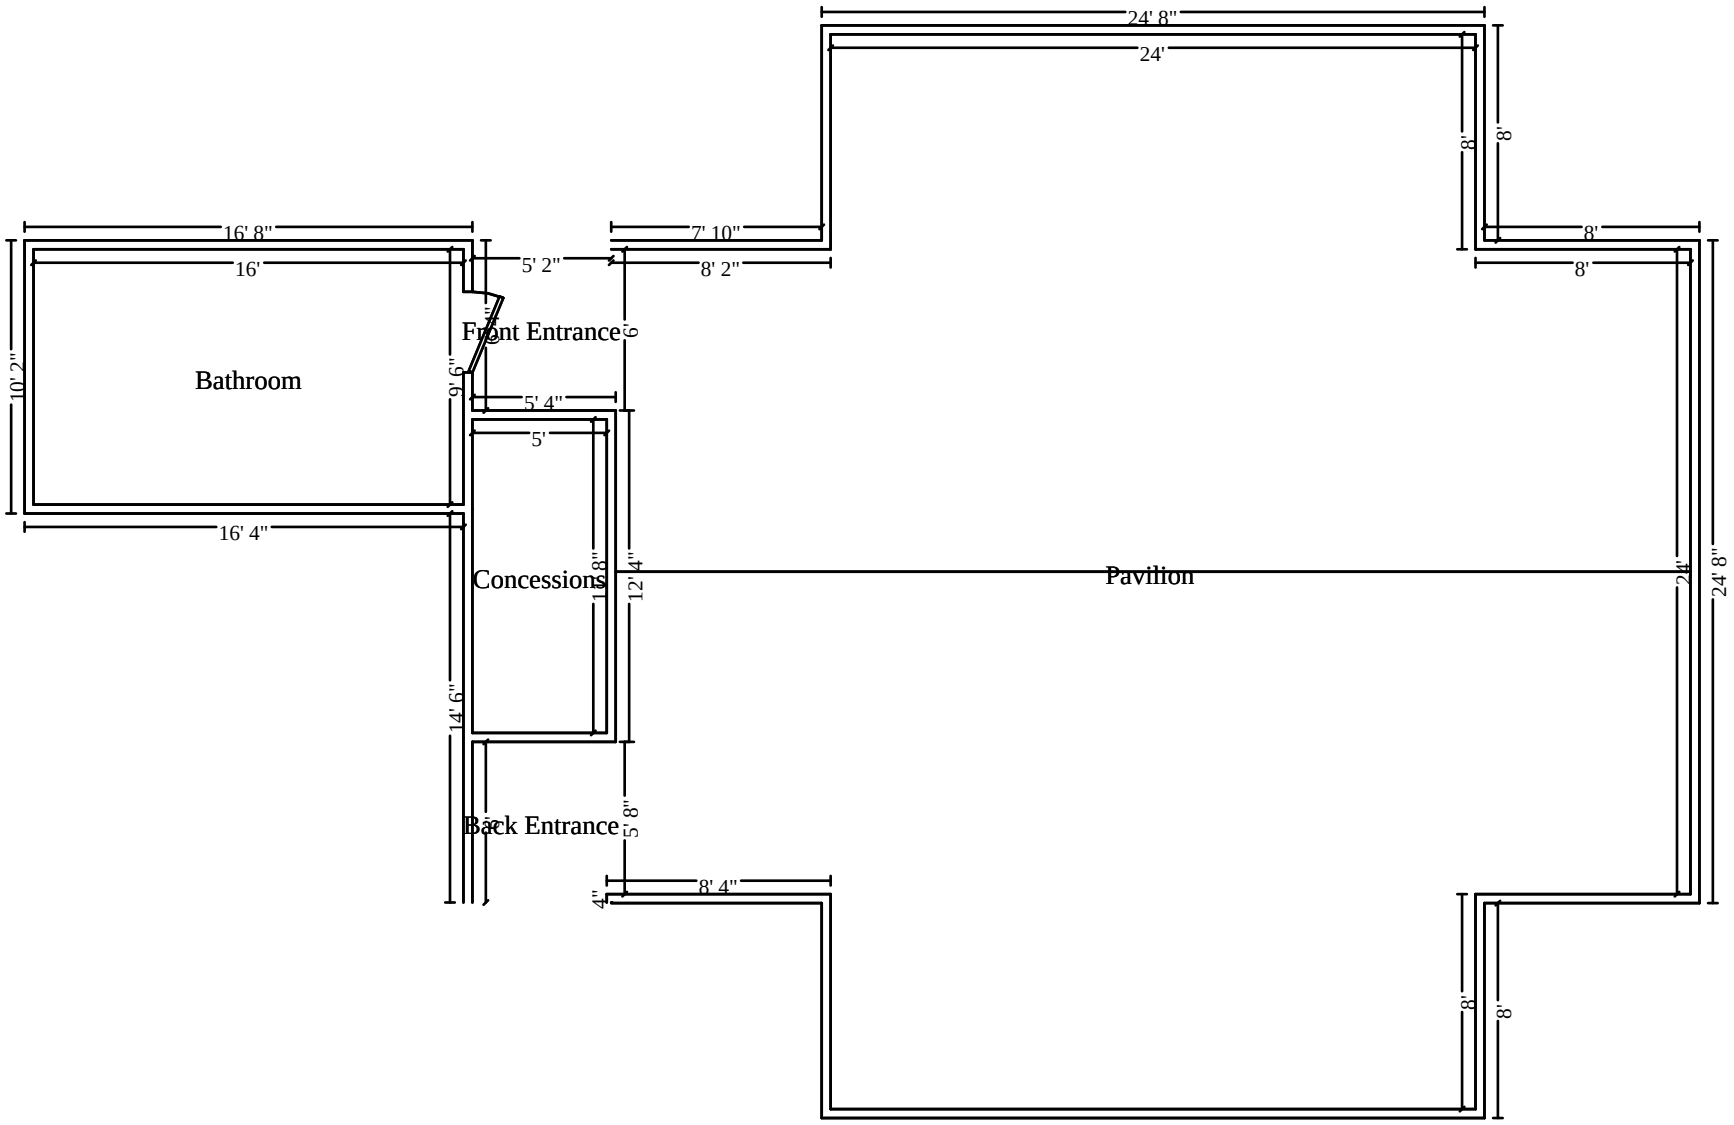
24' 8"
24'
8'
8'
8'
8'
16' 8"
16'
5' 2"
7' 10"
8' 2"
Front Entrance
Bathroom
10' 2"
9' 6"
5' 4"
5'
16' 4"
Concessions
Pavilion
11' 8"
12' 4"
24'
24' 8"
14' 6"
5' 8"
Back Entrance
4"
8' 4"
8'
8'
N

Interior

AGREEMENT BETWEEN

TRAILS PARK AND RECREATION DISTRICT

And

THIS AGREEMENT ("Agreement") is made as of this _____ day of _____, 2026, between the **TRAILS PARK AND RECREATION DISTRICT**, a quasi-municipal corporation and political subdivision of the State of Colorado ("Owner"), whose address is 16799 East Lake Avenue, Centennial, Colorado, 80016, and

_____, a _____ corporation whose address is

_____with a mailing address of ("Contractor"). The Owner and Contractor are sometimes referred to individually herein as a "Party" and collectively as the "Parties."

In consideration of the mutual covenants, agreements, conditions and undertakings hereinafter set forth, Owner and Contractor agree as follows:

Section 1. Scope of Work. Contractor shall perform all work in accordance with the Contract Documents as identified in Section 17 (Contract Documents) for Owner's **Spring Creek Park Pavilion Structural Repair project located at 4001 S. Himalaya St**, Aurora, Colorado 80013, as more particularly described in the Contract Documents, including furnishing all construction plans and methods, construction management, labor, equipment and materials (generally referred to as the "Project"), and shall complete the Project, including any additional work authorized pursuant to Section 16, in accordance with the terms of this Agreement and the Contract Documents. Without limiting the foregoing, Contractor shall (i) engage, at its own cost, a Colorado-licensed Professional Engineer to design the temporary shoring required to support the existing roof framing during the repair; (ii) coordinate with Owner's separately retained special inspection agency and request and schedule all required inspections, provided that the cost of any additional testing or inspection resulting from corrective work shall be borne by Contractor; and (iii) compensate Martin/Martin Consulting Engineers for the design of any Contractor-requested change from the structural drawings, which change shall not proceed until approved and designed by Martin/Martin Consulting Engineers. The Project is an insurance-funded repair, and Contractor shall cooperate with reasonable requests of Owner's insurer and its adjuster, including permitting inspection of the work and furnishing progress photographs and itemized invoices.

Section 2. Contract Price. Owner shall pay Contractor for the performance of work and completion of the Project the total price of _____ ($_____) (the "Contract Price"), subject to certain adjustments as herein provided, in accordance with the bid proposal submitted by Contractor, including the bid alternate for full replacement of

SAMPLE

the roll-up door and keyless entry pad. The Contract Price may be adjusted (i) for changes in the Contract Documents or for extensions of time to complete performance, if approved by Owner and Contractor as specified in Section 16 (Change Orders; Appropriations); (ii) for any additional work authorized pursuant to Section 16 (Change Orders; Appropriations); and (iii) for certain changes in quantities, if bid on a unit-price basis in the bid proposal. All unit quantities requiring an adjustment of the Contract Price shall be verified by Project Manager, as defined in Section 15 (Project Manager).

Section 3. Progress Payments. Owner will make progress payments monthly on account of the Contract Price in accordance with partial payment applications prepared by Contractor for work performed during the last monthly period and which have been approved by Project Manager and Owner. Contractor shall submit partial payment applications for the last completed work period to Project Manager by the first (1st) day of each month. Each partial payment application shall be itemized consistent with the bid item breakdown in Contractor's bid proposal and accompanied by progress photographs of the work performed. Owner shall authorize progress payments for the amount approved by Project Manager and Owner under such partial payment applications on or before the twentieth (20th) day of each month. Progress payments shall not constitute final acceptance of the Project. Owner may withhold progress payments if: (i) Contractor's performance is inadequate or defective and not remedied in accordance with Project Manager's directions; (ii) Contractor does not make prompt and proper disbursements to subcontractors on receipt of progress payments from Owner; (iii) Contractor does not promptly pay for materials, labor or equipment furnished on the Project; (iv) claims or liens are filed on the Project; (v) in Project Manager's opinion, Contractor's performance is not progressing satisfactorily or completion of the Project is jeopardized or delayed; or (vi) Owner has not been supplied with certificates of insurance as required by Section 12.g (Insurance).

Section 4. Retainage. An amount equal to five percent (5%) of each progress payment made on the Contract Price shall be retained by Owner. Such retainage of the Contract Price shall be held by Owner until the Project is completed and finally accepted by Owner in accordance with the provisions hereof. Owner shall pay the full amount of such retainage to Contractor within sixty (60) days of final completion and acceptance of the Project, except to the extent of any claims filed pursuant to Section 38-26-107, C.R.S. Any release of retainage to Contractor or a subcontractor prior to final payment shall, in addition to any other requirements of the Contract Documents, require written approval from the surety furnishing bonds pursuant to Section 13 (Performance, Payment and Warranty Bonds).

Section 5. Final Payment.

a. Upon completion of the Project and Contractor's submittal of notice thereof to Project Manager and Owner, Project Manager shall inspect the Project and reject any portion of performance not in conformity with the Contract Documents. Defective

materials, equipment or work shall be remedied immediately by Contractor before final payment. Owner shall make final payment to Contractor within thirty (30) days after (i) final acceptance of performance by Owner as specified in Section 6 (Final Acceptance) and (ii) receipt of Project Manager's confirmation to Owner that the Project has been completed satisfactorily. Final payment shall not, however, be due until Contractor has delivered to Owner a complete release of all claims or liens against the Project and has produced satisfactory receipts, waivers or lien releases indicating final and total payment to all subcontractors and persons who have furnished materials, labor and equipment on which a lien or claim might potentially be filed in a form acceptable to Owner. **Before making final payment, Owner shall comply with the provisions of Section 38-26-107, C.R.S., including but not limited to, no later than ten (10) days before final payment is made, publish a notice of final payment at least twice in a legal newspaper of general circulation in any county where the work was contracted for or performed**.

b. By making final payment, Owner waives all claims against Contractor, except those expressly declared to Contractor in writing prior to final payment or those arising out of: (i) defective performance appearing after final acceptance; (ii) performance that fails to comply with the Contract Documents, unless expressly waived by Owner in writing; (iii) outstanding claims of any nature, including but not limited to claims for property damage or personal injury arising during the construction period or liens or claims against the Project; or (iv) Contractor's failure to execute any warranty, guarantee or bond or to provide insurance or other defense and indemnification required by the Contract Documents. By accepting final payment, Contractor waives all claims against Owner, except those expressly declared to Owner in writing and received by Owner prior to final payment. Notwithstanding the foregoing, Contractor shall work with Owner in good faith to resolve any claims it may have prior to final payment being made.

Section 6. Final Acceptance.

a. Final acceptance of the Project shall follow inspection and approval of Contractor's performance by Project Manager, along with inspection by appropriate manufacturers' representatives and governmental officials pursuant to local, State, and federal requirements as necessary. Owner shall have the right to determine the acceptability of Contractor's performance and conformance with the Contract Documents, which determination shall be conclusive and binding upon Contractor. Final acceptance by Owner is subject to the provisions of Section 5 (Final Payment) and in no manner affects or releases any warranty or guarantee with Contractor or manufacturers or suppliers of Project equipment or materials.

b. When presented for final acceptance, the Project shall be delivered to Owner in complete compliance with the Contract Documents free from any lien, claim or encumbrance, whether in existence or subsequently established by law, statute, ordinance or otherwise. Notwithstanding the foregoing, nothing in the Contract Documents shall give Contractor or any subcontractor, laborer, supplier, manufacturer or other person or entity,

either expressly or by implication, any right to assert a lien, claim or encumbrance against the Project.

Section 7. Commencement and Completion of Performance; Liquidated Damages.

a. Contractor shall commence performance within ten (10) days after receipt of written Notice to Proceed, which is expected to be given on or before _____, and shall diligently perform all work through completion. Unless an extension of time is granted by Owner as hereinafter set forth, Contractor shall submit a complete building permit application to Arapahoe County within _____ days after the date of written Notice to Proceed, shall substantially complete the building repairs within ninety (90) days after issuance of the building permit, shall complete all site work that cannot be performed due to seasonal temperature limitations, including concrete curb, gutter, and sidewalk replacement, asphalt crack repair, and landscape restoration, no later than May 31, 2027, and shall finally complete the Project within a maximum period of _____ days after the date of Substantial Completion. For purposes of this Agreement, (i) "Substantial Completion" shall be the time at which the Project (or a specified part thereof) has progressed to the point where, in the opinion of Project Manager, the Project (or a specified part thereof) is sufficiently complete in accordance with the Contract Documents, so that the Project (or a specified part thereof) can be utilized by Owner for the purposes for which it is intended; and (ii) "Final Completion" shall be the time at which Owner accepts the Project upon confirmation from Project Manager and Contractor that the Project is totally complete in accordance with Contract Documents.

b. If Contractor fails to perform the Project within the above-referenced performance deadlines or any extension thereof (the "Performance Deadlines"), Contractor shall pay to Owner as liquidated damages (and not as a penalty) for ordinary and general damages and inconvenience (exclusive of any special damages such as, by way of example and not limitation, any liabilities to third parties) the sum of:

1.	Late Substantial Completion:	$1,000.00 per day
2.	Late Final Completion:	$750.00 per day.

These liquidated damages are based upon Owner's evaluation of its likely losses in the event the Performance Deadlines are not met. The liquidated damages herein established are agreed to by Contractor after full discussion of the implication of this Section 7. The failure to perform the work and complete the Project by the Performance Deadlines will cause significant damage to Owner. Owner and Contractor agree that such actual damages caused by Contractor's failure to meet the Performance Deadlines would reasonably likely include, without limitation, the costs for additional construction management and other Owner representative/employee time; the costs for third-party

consultants' time; inefficiency and inconvenience damages to Owner's operations; damages to Owner's reputation with third-parties (including governmental entities with regulatory jurisdiction over Owner), as well as other potential actual damages to Owner reasonably associated with the subject matter of this Agreement. Contractor acknowledges that the liquidated damages established herein are a reasonable pre-estimate of the detriment Owner will suffer in the event Contractor fails to perform the work and complete the Project by the Performance Deadlines and, after a full discussion of the implications of this Section, further acknowledges that the above estimates are reasonable of presumed actual damages given it would be impractical and difficult to precisely ascertain the actual damages that Owner might suffer by reason of Contractor's failure to perform the work and complete the Project by the Performance Deadlines. The liquidated damages established herein are intended to be and are cumulative and shall be in addition to any other remedy enforceable at law under this Agreement. Liquidated damages do not include any sums of money to reimburse Owner for extra costs which Owner may become obligated to pay on other contracts that are delayed or extended because of Contractor's failure to perform the work and complete the Project by the Performance Deadlines. Should Owner incur such other additional costs because of delays or extensions to other contracts resulting from Contractor's unexcused failure or delay in performance, Owner will assess any such extra costs against Contractor in addition to the liquidated damages provided for herein.

c. No extension of time to complete performance shall be granted under normal circumstances. Extensions of time to complete performance may be authorized by Owner in its sole discretion for any actual period of delay on an occurrence basis for: (i) adverse weather or climatic conditions not reasonably anticipated; (ii) major labor disputes; (iii) acts of God; (iv) detrimental acts of Owner; (v) acts of another contractor in the performance of related work under a separate contract with Owner; (vi) delays resulting from the intervention of governmental agencies in the performance of work on the Project, if not caused by Contractor or its subcontractors; or (vii) other extraordinary circumstances beyond Contractor's reasonable control. Foreseeable weather delays and delays or failures in delivery of equipment or materials shall not constitute cause for an extension of time to complete performance or for an adjustment to the Contract Price. Any request for an extension of time to complete performance shall be submitted in writing to Project Manager for Owner's approval within seven (7) days after such occurrence, shall document the conditions causing the delay, and shall be accompanied and supported by a schedule analysis based on the critical path method, which shows how and where the delay occurred on the then-critical path and its effect on any milestone date or the date of Substantial Completion. The decision of Owner shall be conclusive and binding upon Contractor.

Section 8. Default. Owner may give written notice of grounds for default to Contractor at any time if: (i) Contractor fails to perform in an adequate or specified manner or proceeds in willful violation of the Contract Documents or terms of this Agreement, as determined by Project Manager or Owner; (ii) Project Manager advises Owner that

performance of work on the Project is being delayed unnecessarily or that Contractor is executing its responsibilities in bad faith or contrary to the intent of this Agreement; (iii) performance is not fully completed within the period of time specified for completion under Section 7 (Commencement and Completion of Performance; Liquidated Damages); (iv) work to be performed by Contractor is assigned without Owner's consent; (v) the Contractor fails to procure the insurance required hereunder or provide the Owner with Certificates of Insurance, as defined in Section 12.g. (Insurance), within the timeframe provided herein; (vi) Contractor is insolvent or files for bankruptcy; (vii) Contractor makes a general assignment of assets for the benefit of creditors; (viii) a receiver is appointed for Contractor; or (ix) other serious and reasonable cause exists which jeopardizes completion of the Project. If Contractor does not remedy or otherwise correct the grounds for default within such period of time as specified by Owner, Owner may terminate this Agreement and direct Contractor to discontinue any further work on the Project, and Contractor shall immediately stop all work on the Project and forfeit all rights under this Agreement. Owner, in its discretion, may complete the Project, or may request the surety of Contractor to complete the Project, or may contract with others to complete the Project at the expense of Contractor and its surety. Any increase in costs over the Contract Price and any actual and/or special damages incurred by Owner as a consequence of such default, including reasonable attorneys' fees, shall be paid and satisfied in full by Contractor and its surety.

Section 9. Termination. At any time, Owner may, without cause and without prejudice to any other right or remedy hereunder, elect to terminate this Agreement. In such event, Owner shall give written notice of Project termination to Contractor at least five (5) days in advance of the Project termination date. Such notice may include specific instructions as to work to be completed and other winding-up matters. In the absence of any contrary instructions, Contractor shall place no further orders or enter into subcontracts related to the Project, shall terminate all orders and subcontracts to the extent they relate to terminated work, and shall stop work on the date and in accordance with directions specified in the notice. Contractor shall cooperate with Owner to transfer all of Contractor's rights and interests in any orders, subcontracts or work as directed by Owner. Owner shall pay Contractor for the performance of all work through the Project termination date and for such additional amounts as, in the opinion of Project Manager, are reasonable to compensate Contractor for the termination of this Agreement. Final payment to Contractor shall be made in accordance with Section 5 (Final Payment).

Section 10. Taxes, Licenses, Permits, and Regulations. In all operations connected with the Project, Contractor shall pay all fees, charges and taxes imposed by law, except for sales and use taxes from which Owner or the Project are exempt and shall obtain all licenses and permits necessary for completion of the Project, including payment of all fees, unless otherwise specified by the Contract Documents or approved in writing by the Project Manager. Contractor shall comply with all laws, ordinances, codes, rules, and regulations of all governmental authorities, whether local, State or federal, relating to the performance of work on the Project and particularly for compliance with those laws

concerning the environment, stormwater management permits, workmen's compensation, safety and health, labor, immigration and equal employment opportunity. Owner shall, upon request, furnish Contractor with a copy of its certificate of sales and use tax exemption. Owner shall not reimburse Contractor for any sales or use taxes paid to the State or any county or municipality from which Owner or the Project are exempt.

Section 11. Indemnification; No Waiver of Liability or Immunity. Contractor agrees to indemnify, defend, and hold harmless the Owner and its officers, directors, employees, agents, engineers/architects and attorneys from all costs, claims, damages, judgments, losses, liability, and expenses of every nature, including reasonable attorneys' fees, arising at any time from any act or omission of the Contractor, its agents, representatives, subcontractors, or suppliers. Contractor shall upon request of the Owner promptly assume the defense, with defense counsel of Owner's choice and at Contractor's sole expense, of any claim, action, proceeding or suit that is brought against the Owner arising from any act or omission of the Contractor, its agents, representatives, subcontractors, or suppliers. If other persons and/or entities, excluding the Owner and its officers, directors, employees, agents, engineers, architects, and attorneys, at fault exist, Contractor agrees to work in good faith with such persons and/or entities in determining how the Owner's defense costs shall be covered, but under no circumstances shall the Owner be responsible for those costs. Contractor further agrees that, to the extent applicable, indemnification shall only be to the extent and for an amount represented by the degree or percentage of negligence or fault attributable to the Contractor or its agents, representatives, subcontractors, or suppliers. The extent of the Contractor's obligation to indemnify the Owner and its officers, directors, employees, agents, engineers/architects, and attorneys may be determined only after the Contractor's liability or fault has been determined by adjudication, alternative dispute resolution, or otherwise resolved by mutual agreement of the Parties. Contractor's obligations under this Section shall be to the fullest extent permitted by law and shall survive termination or expiration of this Agreement. **Notwithstanding any other provision contained in this Agreement, the Owner does not agree to defend, indemnify, or hold harmless the Contractor or waive or limit its rights and/or claims in any respect regarding the Contractor's liability (either by type of liability or amount).** Owner is relying on and does not waive or intend to waive by any provision of this Agreement, the monetary limitations or any other rights, immunities, defenses, and protections provided by the Colorado Governmental Immunity Act, § 24-10-101 *et seq*., C.R.S., as from time to time amended, or otherwise available to the Owner or its officers or employees. Nothing in this Section shall be construed to require any indemnification that would make this provision void or unenforceable or to eliminate or reduce the indemnification or rights which the Owner has by law.

Section 12. Insurance.

a. During the term of this Agreement, the Contractor shall purchase and maintain, at its own cost and expense, the following:

1. Workers' compensation insurance for its employees, if any, as required by Colorado law with limits of at least $500,000 per injury or illness an employee suffers as a result of providing the services hereunder, with a $500,000 aggregate per occurrence;

2. Employer's liability insurance with limits of at least $500,000 per employee/accident and $1,000,000 aggregate;

3. Commercial general liability insurance covering, without limitation, premises operations, products-completed operations, contractual liability insuring the obligations assumed by the Contractor under this Agreement, personal and advertising injury, and broad form property damage, with limits of at least $1,000,000 per occurrence for bodily injury, death or damage to property; $1,000,000 per occurrence for personal and advertising injury; $1,000,000 products-completed operations aggregate; and $2,000,000 general aggregate;

4. Automobile liability insurance covering all owned, hired and non-owned vehicles used in the performance of the work under this Agreement with a limit of at least $1,000,000 combined per accident for bodily injury and property damage; and

5. Unless otherwise waived by the Owner in writing, builder's risk insurance for protection against damage, explosion, fire, vandalism, theft and other dangers ordinarily included under such coverage, including loss of use resulting therefrom, to the full insurable value of all property, structures, equipment and material of the Owner within the Contractor's control, designating Owner as "loss payee" thereunder.

b. The insurance required herein may be satisfied through any combination of primary and excess/umbrella liability policies.

c. The insurance required herein shall be written by an insurance company or companies that (i) have an A.M. Best Company rating of "A-VII" or better, and (ii) are authorized to issue insurance in the State of Colorado.

d. The Owner, its directors, officers, employees, and Project Manager, shall be endorsed as "Additional Insureds" under the (i) commercial general liability insurance policy for both ongoing and completed performance and/or operations for a period of two (2) years and (ii) automobile liability policy.

e. The Contractor shall provide a waiver of subrogation endorsement, or its equivalent, under the (i) workers' compensation; (ii) commercial general liability; and (iii) automobile liability insurance policies in favor of the Owner, its directors, officers, agents, and employees.

f. All liability insurance policies shall provide that the required coverage shall be primary and non-contributory to other insurance available to the Owner and its directors, officers, agents, and employees. Any insurance maintained by the Owner and its directors, officers, agents, and employees shall be excess of and shall not contribute with the Contractor's insurance.

g. Prior to commencement of work under this Agreement, Contractor shall provide certificates of insurance satisfactory to the Owner that clearly evidence all insurance coverages required herein, including but not limited to endorsements (individually and collectively, "Certificates of Insurance"). Contractor agrees that, until the Owner is supplied with Certificates of Insurance, no payment under this Agreement will be made by the Owner. Contractor will provide the Owner with updated Certificates of Insurance within ten (10) calendar days of the anniversary of the effective date of coverage should that date fall during the term of this Agreement. Failure of the Owner to require Certificates of Insurance or to identify a deficiency in coverage shall not relieve the Contractor from its responsibility to provide the specific insurance coverages set forth herein.

h. Contractor shall require as part of its contract(s) with subcontractors that each subcontractor purchase and maintain insurance of the types and with policy limits no less than those required of Contractor under this Section 12. All general liability policies carried by a subcontractor shall be endorsed to include the Additional Insureds identified above. Each subcontractor shall be required to provide Contractor with certificates of insurance evidencing such coverage prior to commencement of work by a subcontractor. Such certificates of insurance shall be provided to Owner upon request.

i. The insurance policies afforded hereunder shall not be cancelled or allowed to expire unless at least thirty (30) days' prior written notice has been delivered to the Owner, except in the event of cancellation due to non-payment of a premium, in which case notice shall be given to the Owner no later than ten (10) days prior to cancellation of the policy. Upon receipt of any notice of cancellation or non-renewal, the Contractor shall, within five (5) days, procure other policies of insurance as necessary

to comply with this Section 12 and provide Certificates of Insurance evidencing the same to the Owner.

Section 13. Performance, Payment, and Warranty Bond. Prior to commencement of performance, Contractor shall provide to Owner a general performance, payment and warranty bond executed by Contractor and an acceptable corporate surety, or collateral approved by Owner, in the full amount of the Contract Price, including provisions for any adjustment of the Contract Price in accordance with the terms of this Agreement. Such bond shall expressly guarantee: (i) faithful performance of this Agreement and completion of the Project in complete compliance with the Contract Documents; (ii) payment to all persons performing labor and furnishing materials, supplies, tools and equipment in connection with the Project. Contractor shall obtain such bond on Owner's behalf separate and apart from any similar bond or surety or warranty agreement entered into independently between Owner and any manufacturer or supplier. Owner may, in its discretion, require that the bond guaranteeing payment to all persons performing labor and furnishing materials, supplies, tools and equipment in connection with the Project be separate from the bond guaranteeing performance and warranting the work. Notwithstanding anything contained within the bonds to the contrary, such bonds are required, in part, by and shall comply with the minimum requirements of Section 38-26-106, C.R.S.

Section 14. Warranties and Guarantees. Contractor hereby represents, warrants, and guarantees to Owner all workmanship, equipment and materials on or made a part of the Project and its structures for a period of two (2) years following Final Completion of the Project. Such warranty and guarantee shall be construed to include, but is not limited to, representations that all workmanship, equipment, and materials are of good quality, free from any defects or irregularities, and in strict conformity with the Contract Documents. If any defect in workmanship, equipment or materials arises, Contractor shall remedy or otherwise correct such defect without cost to Owner within such reasonable period of time as specified by Owner in writing. If Contractor fails to repair such defect within such period of time as is specified by Owner, Owner may repair such defect or contract for such repairs at the expense of Contractor and its surety. The performance bond specified in Section 13 shall remain in full force and effect during the period of this warranty and guarantee, including any period necessary to remedy or otherwise correct any defects. Contractor shall provide such warranty and guarantee on Owner's behalf separate and apart from other warranties, guarantees and surety agreements entered into independently between Owner and any manufacturer or supplier.

Section 15. Project Manager. Official authority for the administration of all performance under this Agreement is hereby delegated to Owner's engineer, Martin/Martin Consulting Engineers, and Ryan Bailey, ("Project Manager"), unless otherwise provided in the Contract Documents. Throughout the construction period, Project Manager, or one of them, or such other duly authorized representative of Owner, may inspect the Project

and shall consult with Contractor in regard to any inquiries, directions or interpretations of the Contract Documents.

Section 16. Change Orders; Appropriations. Owner has the unilateral right to order additions, deletions, or changes in the work for the Project at any time, so long as such changes are within the general scope of the Project covered by this agreement. Requests for material changes in the Project may be made by Owner, orally or in writing; however, oral requests shall be confirmed by a written request within ten (10) business days after the oral request is first made. If the Owner directs Contractor to proceed with a material change, Contractor shall be paid for the changes as agreed to by the Parties in writing. **Notwithstanding the foregoing, Contractor shall not proceed with any work outside the scope of the Contract Documents without a written Change Order approved by Owner.**

Subject to Section 36 below, this Agreement is subject to Section 24-91-103.6, C.R.S., and in accordance therewith:

a. Owner represents that it has appropriated money equal to or in excess of the Contract Price for the work.

b. Owner shall not issue any Change Order or other directive (other than a clarification) requiring additional compensable work to be performed that will cause the aggregate amount payable under this Agreement to exceed the amount appropriated for the original Contract Price and any subsequent appropriations, unless:

1. Contractor is given written assurance by Owner that lawful appropriations to cover the costs of the additional work have been made and are available prior to performance of the additional work; or

2. Such additional work is covered by the following remedy-granting provision: Contractor may request, in writing, a letter from Owner explaining the expected sources of funding for the additional work. In the event Owner does not provide such written assurance reasonably satisfactory to Contractor within five (5) days of Contractor's request, Contractor may stop work until such time as Owner provides satisfactory assurances. Contractor's acceptance of a Change Order in accordance with any assurances provided under this Section shall not limit or restrict Contractor from making a claim under the Contract Documents for an adjustment in the Contract Price or the Performance Deadlines or otherwise for expenses or damages directly attributable to Contractor's stoppage of the work as permitted hereunder.

c. For any Change Order or other directive (other than a clarification) that requires additional compensable work to be performed, Owner shall reimburse Contractor for Contractor's costs on the periodic basis set forth in the Contract Documents for all additional directed work performed until the Change Order is finalized. In no

instance shall the periodic reimbursement be required before Contractor has submitted an estimate of cost to Owner for the additional compensable work to be performed.

Section 17. Contract Documents. The Contract Documents comprise the entire agreement and contract between Owner and Contractor and consist of (i) this Agreement and any exhibit or addendum hereto; (ii) the Invitation to Bid for the Spring Creek Park Pavilion Structural Repair issued October 14, 2026, and all addenda thereto; (iii) the structural construction documents prepared by Martin/Martin Consulting Engineers, Project No. 26.1101.S.01, dated September 16, 2026 (Sheets S0.1, S0.2, S1.0, and S2.0); (iv) any other documents furnished to Contractor by or at the request of Owner in connection with the Project, including but not limited to notice to bidders, instructions to bidders, bid bond form, bid proposal, performance, payment and maintenance bonds, notice of award, notice to proceed, specifications, plans, drawings, general conditions, supplementary conditions and special conditions, if any, and any addendum to such documents; and (v) any modifications, change orders or other such revisions approved by the Parties in writing or duly authorized after the execution of this Agreement. The insurance adjuster's scope of repairs prepared by Engle Martin (Estimate No. 1000574928) was furnished to bidders for reference only and is not a Contract Document; quantities shown therein are estimates only, and where such scope of repairs differs from the structural construction documents or the Invitation to Bid, the structural construction documents and the Invitation to Bid shall govern.

Section 18. Report of Differing Conditions. If Contractor believes that any technical data on which Contractor is entitled to rely is inaccurate, or any physical condition differs materially from that indicated, reflected or referred to in the Contract Documents, Contractor shall promptly, after becoming aware of such condition and before performing any further work in connection with the Project, notify Project Manager and Owner in writing about such inadequacy or difference. **Changes initiated by Owner or required by concealed or differing site conditions shall be addressed by Change Order pursuant to Section 16 (Change Orders; Appropriations).**

Section 19. Amendment. This Agreement may be amended, from time to time, by agreement between the Parties. No amendment, modification or alteration of this Agreement shall be binding upon the Parties unless the same is in writing and approved by the duly authorized representatives of each Party. No document executed subsequent to this Agreement shall be interpreted to amend, modify or alter the terms of this Agreement, unless express reference to amending the terms of this Agreement is made in such document.

Section 20. Colorado Labor. If the Project is financed in whole or in part by funds of the State or any county, school district or municipality of the State, Colorado labor shall be employed to perform at least eighty percent (80%) of the work, unless such requirement is waived by the Owner in accordance with Section 8-17-101 (1), C.R.S. "Colorado labor" means any person who is a resident of the State at the time of the Project.

A "resident of the State" is a person who can provide a valid Colorado driver's license, a valid State-issued photo identification, or documentation that he or she has resided in Colorado for the last thirty (30) days.

Section 21. Participation in Certified Apprentice Training Program. If the Owner used a prequalification process pursuant to Section 32-1-1805, C.R.S. to select and award the Work, by execution of this Agreement, Contractor represents, warrants, and agrees that the Contractor shall comply with the provisions of Section 32-1-1805(3), C.R.S., relating to access to apprentice training programs certified by the U.S. Department of Labor or a comparable alternative. If the Contract Price is $250,000 or more, Contractor represents, warrants, and agrees that all subcontractors, at any tier, shall have similar access to either a certified program or comparable alternative.

Section 22. Severability. If any term or condition of this Agreement shall, for any reason, be held to be invalid or unenforceable, the invalidity or unenforceability of such term or condition shall not affect any of the remaining provisions of this Agreement.

Section 23. Waiver. No waiver by either Party of any right, term or condition of this Agreement shall be deemed or construed as a waiver of any other right, term or condition, nor shall a waiver of any breach hereof be deemed to constitute a waiver of any subsequent breach, whether of the same or of a different provision of this Agreement.

Section 24. Remedies. None of the remedies provided to either Party under this Agreement shall be required to be exhausted or exercised as a prerequisite to resort to any further relief to which such Party may then be entitled. Every obligation assumed by, or imposed upon, either Party shall be enforceable by any appropriate action, petition or proceeding at law or in equity, including specific performance. If Owner does not pursue a particular remedy contemporaneously with a default and/or any other issue that may arise, the Owner does not waive the right to pursue the remedy at a later date.

Section 25. Counterparts; Electronic Signatures; Electronic Records. This Agreement may be executed in multiple counterparts, each of which shall constitute an original, but all of which shall constitute one and the same document. The Parties consent to the use of electronic signatures and agree that the transaction may be conducted electronically pursuant to the Uniform Electronic Transactions Act, § 24-71.3-101 *et seq.*, C.R.S.

Section 26. Entirety. This Agreement and all other Contract Documents constitute the entire agreement between the Parties concerning the subject matter herein, and all prior negotiations, representations, contracts, understandings or agreements pertaining to such matters are merged into and superseded by this Agreement and the other Contract Documents.

Section 27. Conflicting Provisions; Grant Requirements Control; Interpretation. In the event any provision of this Agreement conflicts with any provision of any other Contract Document, then the provisions of this Agreement shall govern and control such conflicting provisions. If the Project is financed in whole or in part by a federal or State grant, any provision of the Contract Documents that is in conflict with the terms of such grant shall be inapplicable.

Section 28. Assignment. Contractor shall not, at any time, assign any interest in this Agreement to any person or entity without the prior written consent of Owner. The terms of this Agreement shall inure to and be binding upon any successors and assigns of the Parties.

Section 29. Time. Unless otherwise expressly provided, any reference herein to days shall mean calendar days. All times stated in this Agreement are of the essence.

Section 30. Notice. Any notice required hereunder shall be in writing delivered to the applicable Party at the address set forth at the beginning of this Agreement or as changed pursuant to the provisions of this Section.

Section 31. Section Headings. The section headings in this Agreement have been inserted for convenience of reference only and shall not affect the meaning or interpretation of any part of this Agreement.

Section 32. No Third-Party Beneficiaries. The Parties to this Agreement do not intend to extend any benefits to any person not a Party to this Agreement. No person or entity, other than the Parties to this Agreement, shall have any rights, legal or equitable, to enforce or rely on any provision of this Agreement.

Section 33. Duly Authorized Signatories. By execution of this Agreement, the undersigned each individually represent that he or she is duly authorized to execute and deliver this Agreement and that the subject Party shall be bound by the signatory's execution of this Agreement.

Section 34. Law; **Venue.** The laws of the State of Colorado shall govern the construction, interpretation, execution and enforcement of this Agreement. Venue for any dispute between the Parties arising out of or relating to this Agreement shall be in the State of Colorado District Court for Arapahoe County.

Section 35. Not Construed Against Drafter. Each Party acknowledges that it has had an adequate opportunity to review each and every provision contained in this Agreement, including the opportunity to consult with legal counsel. Based on the foregoing, no provision of this Agreement shall be construed against either Party by reason of such Party being deemed to have drafted such provision.

Section 36. No Multi-Fiscal Year Obligations. Performance of this Agreement extends over multiple fiscal years of the Owner. Accordingly, no provision of this Agreement shall be construed or interpreted as creating an indebtedness or a multiple fiscal year direct or indirect debt, or other multiple year financial obligation whatsoever of Owner within the meaning of any constitutional or statutory debt limitation provision, including, without limitation, Article XI, §§ 1, 2 and 6, and Article X, § 20 of the Colorado Constitution. This Agreement shall not directly or indirectly obligate the Owner to make any payment beyond the funds legally available to it for the then current fiscal year. No provision of this Agreement shall be construed to pledge or create a lien on any class or source of monies of the Owner, nor shall any provision of this Agreement restrict or limit the discretion of the Owner in budgeting and appropriating its funds. The Owner shall notify Contractor if funds are exhausted for any fiscal year, and Contractor may, at its discretion, decide whether to continue working for Owner in that fiscal year.

[Signature Pages Follow]

IN WITNESS WHEREOF, the Parties have executed this Agreement on the day and year first above written.

OWNER:

TRAILS PARK AND RECREATION, a quasi-municipal corporation and political subdivision of the State of Colorado

By: _____
XX / Deputy/Executive Director

STATE OF COLORADO)
) ss.
COUNTY OF ARAPAHOE)

The foregoing Agreement was acknowledged before me this ____ day of _____, 2026, by <Name> as <Title> Director of the Trails Park and Recreation District.

Witness my hand and official seal.

My commission expires: _____

_____
Notary Public

CONTRACTOR:

_____., a
_____corporation

By: _____
Name: _____
Title: _____

STATE OF COLORADO)
) ss.
COUNTY OF _____)

The foregoing Agreement was acknowledged before me this _____ day of _____, 2026, by _____ as _____ of _____a _____ corporation.

Witness my hand and official seal.

My commission expires: _____

_____
Notary Public
